

Impact sheets for selected major Temporary Capacity Restrictions (TCR)



Foreword

On RFC Rhine Alpine we introduced the **TCR Impact sheets** to present in one glance general and important information about upcoming TCRs. These impact sheets highlight **some infrastructure works which have a big impact** on international rail freight traffic along RFC Rhine-Alpine.

Disclaimer:

The content of this document has been compiled with meticulous care based on information available at the publication date. However we cannot assume any liability for accuracy and accept no liability for damages suffered as a result of defects of this document.

For detailed and complete customer information we kindly refer to the information which is available via the involved national Infrastructure Managers.

Further information (e.g. in form of an excel list on all planned TCR) is available on the website of RFC RALP under link: <https://www.corridor-rhine-alpine.eu/downloads.html>

Version 2.0 for timetable 2024, 2025 and 2026

Publication Date: October 2024

PARTNER




Co-financed by the European Union
Connecting Europe Facility

Impact of TCR 2024 at ProRail

Section Venlo - Gremberg



State of play : 01.10.2024
Disclaimer see front page

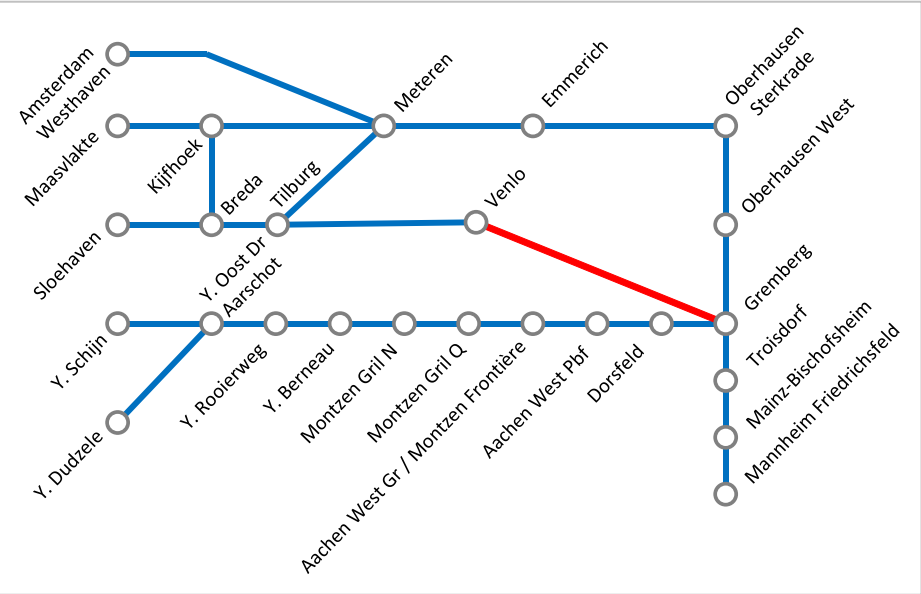

Major Capacity Restriction

- Section: Venlo – Venlo border
- Type: Total closure
- Type of Works: construction of tunnel, removal of railroad crossing
- Periods: see calendar

2024 Calendar

Single track operation Total closure

January							February							March							April						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7	1	2	3	4	5	6	7	1	2	3	4	5	6	7	1	2	3	4	5	6	7
8	9	10	11	12	13	14	8	9	10	11	12	13	14	8	9	10	11	12	13	14	8	9	10	11	12	13	14
15	16	17	18	19	20	21	15	16	17	18	19	20	21	15	16	17	18	19	20	21	15	16	17	18	19	20	21
22	23	24	25	26	27	28	22	23	24	25	26	27	28	22	23	24	25	26	27	28	22	23	24	25	26	27	28
29	30	31					26	27	28	29				25	26	27	28	29	30	31	29	30					

May							June							July							August						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	5					1	2		1	2	3	4	5	6	7				1	2	3	4
6	7	8	9	10	11	12	3	4	5	6	7	8	9	8	9	10	11	12	13	14	5	6	7	8	9	10	11
13	14	15	16	17	18	19	10	11	12	13	14	15	16	15	16	17	18	19	20	21	12	13	14	15	16	17	18
20	21	22	23	24	25	26	17	18	19	20	21	22	23	22	23	24	25	26	27	28	19	20	21	22	23	24	25
27	28	29	30	31			24	25	26	27	28	29	30	29	30	31					26	27	28	29	30	31	

September							October							November							December						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
						1																					1
2	3	4	5	6	7	8	7	8	9	10	11	12	13	4	5	6	7	8	9	10	2	3	4	5	6	7	8
9	10	11	12	13	14	15	14	15	16	17	18	19	20	11	12	13	14	15	16	17	9	10	11	12	13	14	15
16	17	18	19	20	21	22	21	22	23	24	25	26	27	18	19	20	21	22	23	24	16	17	18	19	20	21	22
23	24	25	26	27	28	29	28	29	30	31				25	26	27	28	29	30		23	24	25	26	27	28	29
30																					30	31					

Impact on International Rail Freight


- Deviations: via Betuweroute
- Estimated extra running time: 15-30 minutes
- Restrictions for ad-hoc requests: limited capacity on Betuweroute - Oberhausen
- Restrictions in train parameters: no
- Restrictions in container profile: no
- In annual timetable: no, timetables adapted 4 weeks before operation

Impact of TCR 2024 at ProRail

Section Tilburg - Venlo



State of play : 01.10.2024
Disclaimer see front page

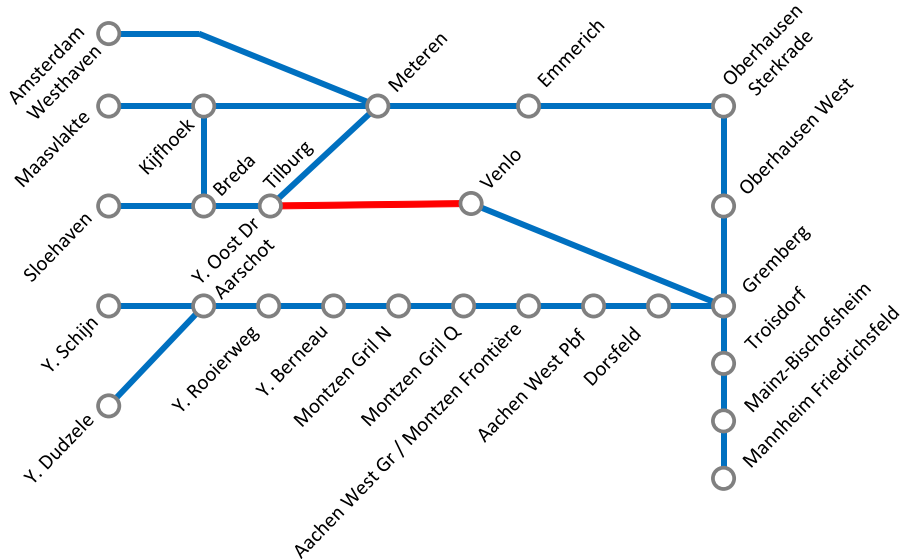

Major Capacity Restriction

- Section: Eindhoven - Venlo
- Type: Total closure
- Type of Works: renewal of infra
- Periods: 09.03.2024 – 19.03.2024

2024 Calendar

Single track operation Total closure

January							February							March							April						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7	1	2	3	4	5	6	7	1	2	3	4	5	6	7	1	2	3	4	5	6	7
8	9	10	11	12	13	14	8	9	10	11	12	13	14	8	9	10	11	12	13	14	8	9	10	11	12	13	14
15	16	17	18	19	20	21	15	16	17	18	19	20	21	15	16	17	18	19	20	21	15	16	17	18	19	20	21
22	23	24	25	26	27	28	22	23	24	25	26	27	28	22	23	24	25	26	27	28	22	23	24	25	26	27	28
29	30	31					26	27	28	29				25	26	27	28	29	30	31	29	30					

May							June							July							August						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
			1	2	3	4					1	2												1	2	3	4
6	7	8	9	10	11	12	3	4	5	6	7	8	9	8	9	10	11	12	13	14	5	6	7	8	9	10	11
13	14	15	16	17	18	19	10	11	12	13	14	15	16	15	16	17	18	19	20	21	12	13	14	15	16	17	18
20	21	22	23	24	25	26	17	18	19	20	21	22	23	22	23	24	25	26	27	28	19	20	21	22	23	24	25
27	28	29	30	31			24	25	26	27	28	29	30	29	30	31					26	27	28	29	30	31	

September							October							November							December						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
						1																					1
2	3	4	5	6	7	8	7	8	9	10	11	12	13	4	5	6	7	8	9	10	2	3	4	5	6	7	8
9	10	11	12	13	14	15	14	15	16	17	18	19	20	11	12	13	14	15	16	17	9	10	11	12	13	14	15
16	17	18	19	20	21	22	21	22	23	24	25	26	27	18	19	20	21	22	23	24	16	17	18	19	20	21	22
23	24	25	26	27	28	29	28	29	30	31				25	26	27	28	29	30		23	24	25	26	27	28	29
30														30	31						30	31					

Impact on International Rail Freight


- Deviations: via Betuweroute
- Estimated extra running time: 15-30 minutes
- Restrictions for ad-hoc requests: limited capacity on Betuweroute - Oberhausen
- Restrictions in train parameters: no
- Restrictions in container profile: no
- In annual timetable: no, timetables adapted 4 weeks before operation

Impact of TCR 2024 at ProRail

Section Breda - Tilburg



State of play : 01.10.2024
Disclaimer see front page

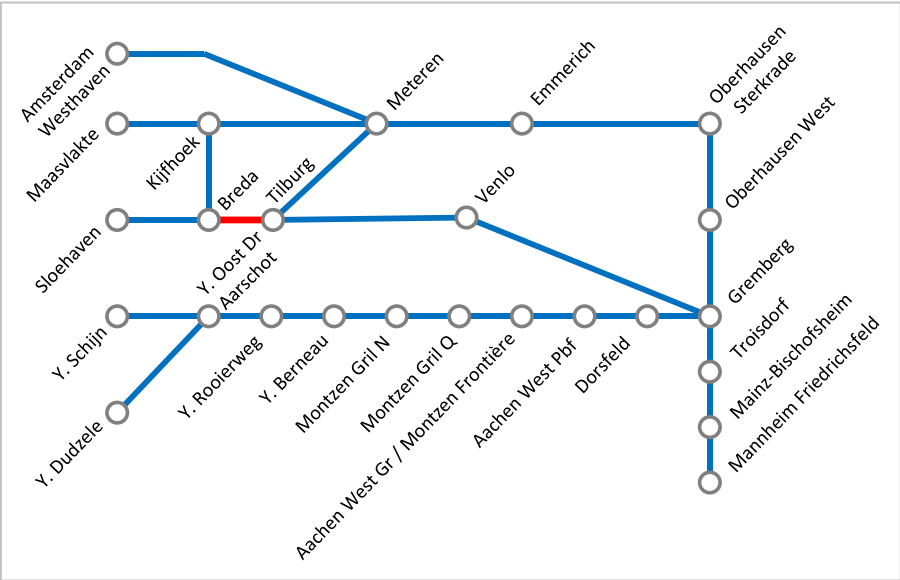

Major Capacity Restriction

- Section: Breda - Tilburg
- Type: Total closure
- Type of Works: renewal of catenary
- Periods: 28.04.2024 – 13.05.2024

2024 Calendar

Single track operation Total closure

January							February							March							April						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7	1	2	3	4	5	6	7	1	2	3	4	5	6	7	1	2	3	4	5	6	7
8	9	10	11	12	13	14	8	9	10	11	12	13	14	8	9	10	11	12	13	14	8	9	10	11	12	13	14
15	16	17	18	19	20	21	15	16	17	18	19	20	21	15	16	17	18	19	20	21	15	16	17	18	19	20	21
22	23	24	25	26	27	28	22	23	24	25	26	27	28	22	23	24	25	26	27	28	22	23	24	25	26	27	28
29	30	31					26	27	28	29				25	26	27	28	29	30	31	29	30					

May							June							July							August						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
			1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25
6	7	8	9	10	11	12	3	4	5	6	7	8	9	1	2	3	4	5	6	7	10	11	12	13	14	15	16
13	14	15	16	17	18	19	10	11	12	13	14	15	16	8	9	10	11	12	13	14	17	18	19	20	21	22	
20	21	22	23	24	25	26	17	18	19	20	21	22	23	15	16	17	18	19	20	21	24	25	26	27	28	29	
27	28	29	30	31			24	25	26	27	28	29	30	22	23	24	25	26	27	28	31						

September							October							November							December						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
						1																				1	
2	3	4	5	6	7	8	7	8	9	10	11	12	13	4	5	6	7	8	9	10	2	3	4	5	6	7	
9	10	11	12	13	14	15	14	15	16	17	18	19	20	11	12	13	14	15	16	17	9	10	11	12	13	14	
16	17	18	19	20	21	22	21	22	23	24	25	26	27	18	19	20	21	22	23	24	16	17	18	19	20	21	
23	24	25	26	27	28	29	28	29	30	31				25	26	27	28	29	30		23	24	25	26	27	28	
30																					30	31					

Impact on International Rail Freight


- Deviations: via Betuweroute
- Estimated extra running time: 15-30 minutes
- Restrictions for ad-hoc requests: limited capacity on Betuweroute - Oberhausen
- Restrictions in train parameters: no
- Restrictions in container profile: no
- In annual timetable: no, timetables adapted 4 weeks before operation

Impact of TCR 2024 at ProRail

Section Tilburg - Venlo



State of play : 01.10.2024
Disclaimer see front page

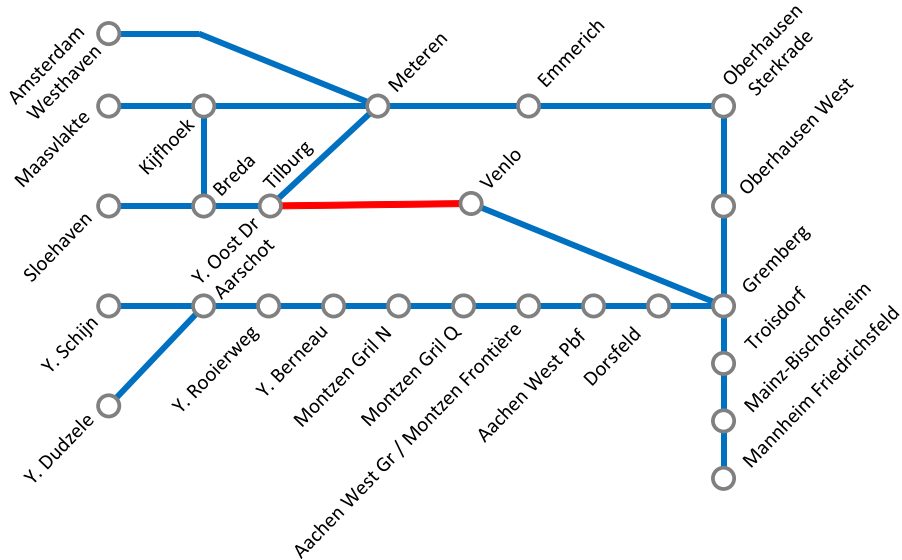

Major Capacity Restriction

- Section: Tilburg - Boxtel
- Type: Total closure
- Type of Works: renewal of infra
- Periods: 19.10.2024 – 25.10.2024

2024 Calendar

Single track operation Total closure

January							February							March							April						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7				1	2	3	4					1	2	3				1	2	3	4
8	9	10	11	12	13	14	5	6	7	8	9	10	11	4	5	6	7	8	9	10	8	9	10	11	12	13	14
15	16	17	18	19	20	21	12	13	14	15	16	17	18	11	12	13	14	15	16	17	15	16	17	18	19	20	21
22	23	24	25	26	27	28	19	20	21	22	23	24	25	18	19	20	21	22	23	24	22	23	24	25	26	27	28
29	30	31					26	27	28	29				25	26	27	28	29	30	31	29	30					

May							June							July							August						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
			1	2	3	4						1	2											1	2	3	4
6	7	8	9	10	11	12	3	4	5	6	7	8	9	6	7	8	9	10	11	12	13	14	15	16	17	18	19
13	14	15	16	17	18	19	10	11	12	13	14	15	16	13	14	15	16	17	18	19	20	21	22	23	24	25	26
20	21	22	23	24	25	26	17	18	19	20	21	22	23	20	21	22	23	24	25	26	27	28	29	30	31		
27	28	29	30	31			24	25	26	27	28	29	30	27	28	29	30	31			26	27	28	29	30	31	

September							October							November							December						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
						1																					1
2	3	4	5	6	7	8	7	8	9	10	11	12	13	4	5	6	7	8	9	10	2	3	4	5	6	7	8
9	10	11	12	13	14	15	14	15	16	17	18	19	20	11	12	13	14	15	16	17	9	10	11	12	13	14	15
16	17	18	19	20	21	22	21	22	23	24	25	26	27	18	19	20	21	22	23	24	16	17	18	19	20	21	22
23	24	25	26	27	28	29	28	29	30	31				25	26	27	28	29	30		23	24	25	26	27	28	29
30																					30	31					


Impact on International Rail Freight

- Deviations: via Betuweroute
- Estimated extra running time: 15-30 minutes
- Restrictions for ad-hoc requests: limited capacity on Betuweroute - Oberhausen
- Restrictions in train parameters: no
- Restrictions in container profile: no
- In annual timetable: no, timetables adapted 4 weeks before operation

Impact of TCR 2024 at Infrabel Section Antwerpen - Montzen



State of play : 01.10.2024
Disclaimer see front page

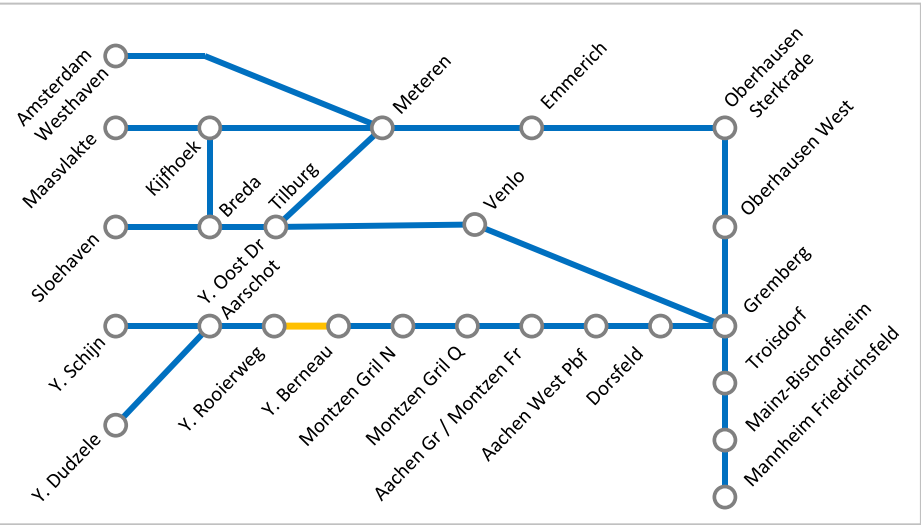

Major Capacity Restriction

- Location: Bassenge - Y. Glons
- Single track operation
- Period: 15.04.2024 (7:00) - 09.06.2024 (22:00)
- Major works on bridge

2024 Calendar

Single track operation Total closure

January							February							March							April						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7	1	2	3	4	5	6	7	1	2	3	4	5	6	7	1	2	3	4	5	6	7
8	9	10	11	12	13	14	8	9	10	11	12	13	14	8	9	10	11	12	13	14	8	9	10	11	12	13	14
15	16	17	18	19	20	21	15	16	17	18	19	20	21	15	16	17	18	19	20	21	15	16	17	18	19	20	21
22	23	24	25	26	27	28	22	23	24	25	26	27	28	22	23	24	25	26	27	28	22	23	24	25	26	27	28
29	30	31					26	27	28	29				25	26	27	28	29	30	31	29	30					

May							June							July							August						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
			1	2	3	4	1	2	3	4	5	6	7	1	2	3	4	5	6	7	1	2	3	4	5	6	7
6	7	8	9	10	11	12	8	9	10	11	12	13	14	8	9	10	11	12	13	14	5	6	7	8	9	10	11
13	14	15	16	17	18	19	15	16	17	18	19	20	21	15	16	17	18	19	20	21	12	13	14	15	16	17	18
20	21	22	23	24	25	26	22	23	24	25	26	27	28	22	23	24	25	26	27	28	19	20	21	22	23	24	25
27	28	29	30	31			29	30	31					29	30	31					26	27	28	29	30	31	


September							October							November							December						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
						1	1	2	3	4	5	6	7					1	2	3						1	
2	3	4	5	6	7	8	7	8	9	10	11	12	13	4	5	6	7	8	9	10	2	3	4	5	6	7	8
9	10	11	12	13	14	15	14	15	16	17	18	19	20	11	12	13	14	15	16	17	9	10	11	12	13	14	15
16	17	18	19	20	21	22	21	22	23	24	25	26	27	18	19	20	21	22	23	24	16	17	18	19	20	21	22
23	24	25	26	27	28	29	28	29	30	31				25	26	27	28	29	30		23	24	25	26	27	28	29
30																					30	31					

Impact on International Rail Freight

- Deviations: No
- Estimated extra running time: tbd
- Restrictions for ad-hoc requests: no
- Restrictions in train parameters: no
- Restrictions in container profile: No
- In annual timetable: Yes



State of play : 01.10.2024
Disclaimer see front page

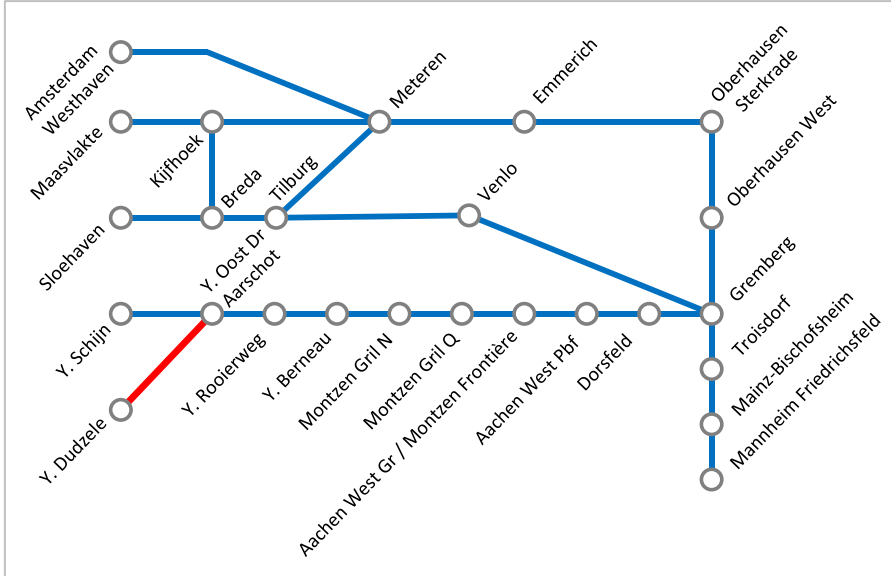

Major Capacity Restriction

- Section: Londerzeel - Mechelen
- Type: Total Closure
- Periods : 10.02.2024 (06:00) – 19.02.2024 (4:00)
And 26.10.2024 (00:30) – 04.11.2024 (4:00)
- Type of works: Signalling ETCS

2024 Calendar

 Single track operation  Total closure

January						
Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7
8	9	10	11	12	13	14
15	16	17	18	19	20	21
22	23	24	25	26	27	28
29	30	31				

February						
Mo	Tu	We	Th	Fr	Sa	Su
			1	2	3	4
5	6	7	8	9	10	11
12	13	14	15	16	17	18
19	20	21	22	23	24	25
26	27	28	29			

March						
Mo	Tu	We	Th	Fr	Sa	Su
			1	2	3	
4	5	6	7	8	9	10
11	12	13	14	15	16	17
18	19	20	21	22	23	24
25	26	27	28	29	30	31

April						
Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7
8	9	10	11	12	13	14
15	16	17	18	19	20	21
22	23	24	25	26	27	28
29	30					

May						
Mo	Tu	We	Th	Fr	Sa	Su
			1	2	3	4
6	7	8	9	10	11	12
13	14	15	16	17	18	19
20	21	22	23	24	25	26
27	28	29	30	31		

June						
Mo	Tu	We	Th	Fr	Sa	Su
					1	2
3	4	5	6	7	8	9
10	11	12	13	14	15	16
17	18	19	20	21	22	23
24	25	26	27	28	29	30

July						
Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7
8	9	10	11	12	13	14
15	16	17	18	19	20	21
22	23	24	25	26	27	28
29	30	31				

August						
Mo	Tu	We	Th	Fr	Sa	Su
				1	2	3
5	6	7	8	9	10	11
12	13	14	15	16	17	18
19	20	21	22	23	24	25
26	27	28	29	30	31	

September						
Mo	Tu	We	Th	Fr	Sa	Su
						1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	29
30						

October						
Mo	Tu	We	Th	Fr	Sa	Su
	1	2	3	4	5	6
7	8	9	10	11	12	13
14	15	16	17	18	19	20
21	22	23	24	25	26	27
28	29	30	31			

November						
Mo	Tu	We	Th	Fr	Sa	Su
				1	2	3
4	5	6	7	8	9	10
11	12	13	14	15	16	17
18	19	20	21	22	23	24
25	26	27	28	29	30	

December						
Mo	Tu	We	Th	Fr	Sa	Su
						1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	29
30	31					

Impact on International Rail Freight


- Deviations: L15-L59
- Estimated extra running time: TbD
- Restrictions for ad-hoc requests: no
- Restrictions in train parameters: no
- Restrictions in container profile: no
- In annual timetable: no, timetables adapted at the latest 4 weeks before operation

Impact of TCR 2024 at DB InfraGO AG

Section Emmerich Border - Oberhausen Main Station



State of play : 01.10.2024
Disclaimer see front page

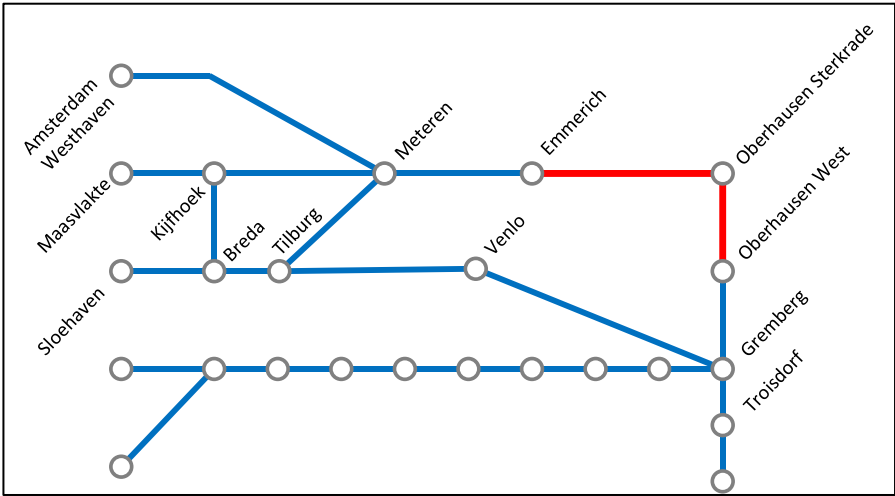

Major Capacity Restriction

- Location: Emmerich Border - Oberhausen Main Station
- Type: Single Track Operation (Until Oct only at night, from Nov on continuous) and Total Closures
- Period: Jan/Feb, May-Dec. 2024 (&2025 ff.)
- Type of works: Track & Rail, Bridge, Catenary, Switch, Miscellaneous

2024 Calendar

Single track operation Total closure

January							February							March							April						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7	1	2	3	4				1	2	3					1	2	3	4	5	6	7
8	9	10	11	12	13	14	5	6	7	8	9	10	11	4	5	6	7	8	9	10	8	9	10	11	12	13	14
15	16	17	18	19	20	21	12	13	14	15	16	17	18	11	12	13	14	15	16	17	15	16	17	18	19	20	21
22	23	24	25	26	27	28	19	20	21	22	23	24	25	18	19	20	21	22	23	24	22	23	24	25	26	27	28
29	30	31					26	27	28	29				25	26	27	28	29	30	31	29	30					

May							June							July							August						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
			1	2	3	4						1	2											1	2	3	4
6	7	8	9	10	11	12	3	4	5	6	7	8	9	8	9	10	11	12	13	14	5	6	7	8	9	10	11
13	14	15	16	17	18	19	10	11	12	13	14	15	16	15	16	17	18	19	20	21	12	13	14	15	16	17	18
20	21	22	23	24	25	26	17	18	19	20	21	22	23	22	23	24	25	26	27	28	19	20	21	22	23	24	25
27	28	29	30	31			24	25	26	27	28	29	30	29	30	31					26	27	28	29	30	31	

September							October							November							December						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
						1																					1
2	3	4	5	6	7	8	7	8	9	10	11	12	13	4	5	6	7	8	9	10	2	3	4	5	6	7	8
9	10	11	12	13	14	15	14	15	16	17	18	19	20	11	12	13	14	15	16	17	9	10	11	12	13	14	15
16	17	18	19	20	21	22	21	22	23	24	25	26	27	18	19	20	21	22	23	24	16	17	18	19	20	21	22
23	24	25	26	27	28	29	28	29	30	31				25	26	27	28	29	30		23	24	25	26	27	28	29
30																					30	31					

Impact on International Rail Freight

- Cancellations: Yes
- Deviations: Yes
- Estimated extra running time: Detailed information on extra running time is distributed by DB InfraGO individually for every customer for each affected train. Additionally DB InfraGO offers train path advice free of charge
- In annual timetable: No

Impact of TCR 2024 at DB InfraGO AG

Section Karlsruhe – Offenburg (Rhine Valley)



State of play : 01.10.2024
Disclaimer see front page



2024 Calendar

Single track operation Total closure

January							February							March							April						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7				1	2	3	4					1	2	3	1	2	3	4	5	6	7
8	9	10	11	12	13	14	5	6	7	8	9	10	11	4	5	6	7	8	9	10	8	9	10	11	12	13	14
15	16	17	18	19	20	21	12	13	14	15	16	17	18	11	12	13	14	15	16	17	15	16	17	18	19	20	21
22	23	24	25	26	27	28	19	20	21	22	23	24	25	18	19	20	21	22	23	24	22	23	24	25	26	27	28
29	30	31					26	27	28	29				25	26	27	28	29	30	31	29	30					

May							June							July							August						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	5						1	2														
6	7	8	9	10	11	12	3	4	5	6	7	8	9	8	9	10	11	12	13	14	5	6	7	8	9	10	11
13	14	15	16	17	18	19	10	11	12	13	14	15	16	15	16	17	18	19	20	21	12	13	14	15	16	17	18
20	21	22	23	24	25	26	17	18	19	20	21	22	23	22	23	24	25	26	27	28	19	20	21	22	23	24	25
27	28	29	30	31			24	25	26	27	28	29	30	29	30	31					26	27	28	29	30	31	

September							October							November							December						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
						1		1	2	3	4	5	6					1	2	3							
2	3	4	5	6	7	8	7	8	9	10	11	12	13	4	5	6	7	8	9	10	2	3	4	5	6	7	8
9	10	11	12	13	14	15	14	15	16	17	18	19	20	11	12	13	14	15	16	17	9	10	11	12	13	14	15
16	17	18	19	20	21	22	21	22	23	24	25	26	27	18	19	20	21	22	23	24	16	17	18	19	20	21	22
23	24	25	26	27	28	29	28	29	30	31				25	26	27	28	29	30		23	24	25	26	27	28	29
30																					30	31					

Major Capacity Restriction

- Section: Raststatt Süd – Baden-Baden
- Typ: Total Closure
- Period: Aug – Sep 2024
- Type of works: Signal, Track & Rail, Bridge, Switch, Miscellaneous

Impact on International Rail Freight


- Cancellations: Yes
- Deviations: Yes
- Estimated extra running time: Detailed information on extra running time is distributed by DB InfraGO individually for every customer for each affected train. Additionally DB InfraGO offers train path advice free of charge
- In annual timetable: Yes

Impact of TCR 2024 at SBB Infra/BLS Netz (1)

Section Spiez – Brig (Mountain line)



State of play : 01.10.2024
Disclaimer see front page

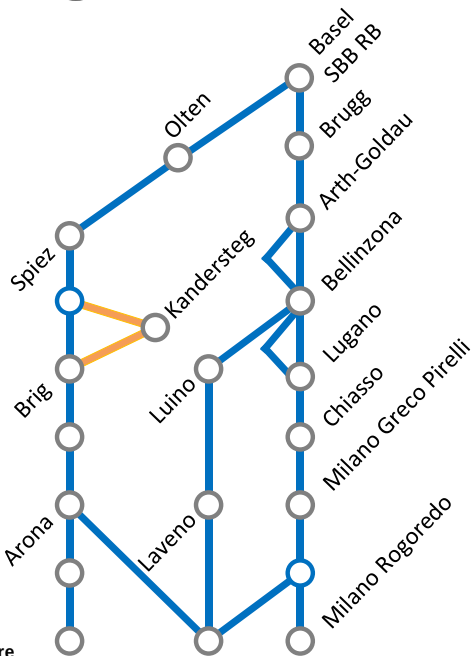

Major Capacity Restriction

- Section: SPIEZ – BRIG (mountain line)
- Type: ¼ tunnel closure with partially single-track
- Type of Works: Tunnel renewal
- Period: From 31/07/2018 to 21/12/2024

2024 Calendar

Single track operation Total closure

January							February							March							April						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7						1	2	3							1	2	3	4	5	6	7
8	9	10	11	12	13	14	5	6	7	8	9	10	11	4	5	6	7	8	9	10	8	9	10	11	12	13	14
15	16	17	18	19	20	21	12	13	14	15	16	17	18	11	12	13	14	15	16	17	15	16	17	18	19	20	21
22	23	24	25	26	27	28	19	20	21	22	23	24	25	18	19	20	21	22	23	24	22	23	24	25	26	27	28
29	30	31					26	27	28	29				25	26	27	28	29	30	31	29	30					

May							June							July							August						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	5						1	2	1	2	3	4	5	6	7				1	2	3	4
6	7	8	9	10	11	12	3	4	5	6	7	8	9	8	9	10	11	12	13	14	5	6	7	8	9	10	11
13	14	15	16	17	18	19	10	11	12	13	14	15	16	15	16	17	18	19	20	21	12	13	14	15	16	17	18
20	21	22	23	24	25	26	17	18	19	20	21	22	23	22	23	24	25	26	27	28	19	20	21	22	23	24	25
27	28	29	30	31			24	25	26	27	28	29	30	29	30	31					26	27	28	29	30	31	

September							October							November							December						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
						1						1	2	3	4	5	6	7	8	9	2	3	4	5	6	7	8
2	3	4	5	6	7	8	7	8	9	10	11	12	13	4	5	6	7	8	9	10	9	10	11	12	13	14	15
9	10	11	12	13	14	15	14	15	16	17	18	19	20	11	12	13	14	15	16	17	16	17	18	19	20	21	22
16	17	18	19	20	21	22	21	22	23	24	25	26	27	18	19	20	21	22	23	24	23	24	25	26	27	28	29
23	24	25	26	27	28	29	28	29	30	31				25	26	27	28	29	30		30	31					

Impact on International Rail Freight


- Reduction of available capacity; possible delays due speed reduction
- Marginal residual capacity during works
- in the annual TT: Yes
- Extra running time max 15 Min
- Profile restrictions No

Impact of TCR 2024 at SBB Infra/BLS Netz (2)

Section Arth-Goldau – Bellinzona (Gotthard base tunnel)



State of play : 01.10.2024
Disclaimer see front page

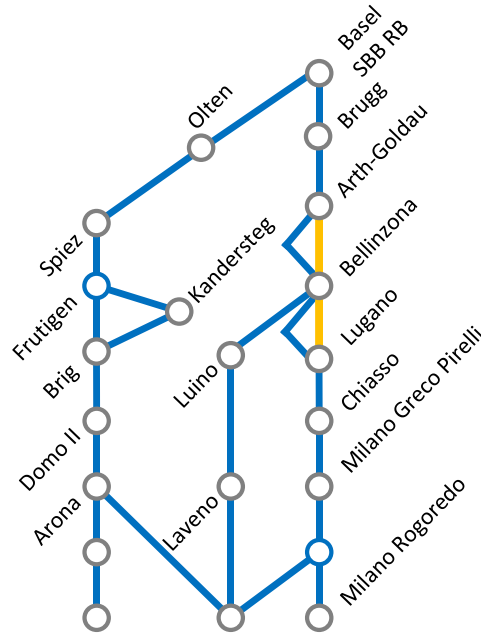

Major Capacity Restriction

- Section: Arth-Goldau – Bellinzona (base tunnel)
- Type: 1/2 tunnel closure with partially single-track
- Type of Works: renewal tunnel equipment
- Period: From 10.08.2023 to 02.09.2024

2024 Calendar

Single track operation Total closure

January							February							March							April						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7								1	2	3					1	2	3	4	5	6	7
8	9	10	11	12	13	14	5	6	7	8	9	10	11	4	5	6	7	8	9	10	8	9	10	11	12	13	14
15	16	17	18	19	20	21	12	13	14	15	16	17	18	11	12	13	14	15	16	17	15	16	17	18	19	20	21
22	23	24	25	26	27	28	19	20	21	22	23	24	25	18	19	20	21	22	23	24	22	23	24	25	26	27	28
29	30	31					26	27	28	29				25	26	27	28	29	30	31	29	30					

May							June							July							August						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	5						1	2	1	2	3	4	5	6	7				1	2	3	4
6	7	8	9	10	11	12	3	4	5	6	7	8	9	8	9	10	11	12	13	14	5	6	7	8	9	10	11
13	14	15	16	17	18	19	10	11	12	13	14	15	16	15	16	17	18	19	20	21	12	13	14	15	16	17	18
20	21	22	23	24	25	26	17	18	19	20	21	22	23	22	23	24	25	26	27	28	19	20	21	22	23	24	25
27	28	29	30	31			24	25	26	27	28	29	30	29	30	31					26	27	28	29	30	31	

September							October							November							December						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
					1		1	2	3	4	5	6		1	2	3					2	3	4	5	6	7	8
2	3	4	5	6	7	8	7	8	9	10	11	12	13	4	5	6	7	8	9	10	9	10	11	12	13	14	15
9	10	11	12	13	14	15	14	15	16	17	18	19	20	11	12	13	14	15	16	17	16	17	18	19	20	21	22
16	17	18	19	20	21	22	21	22	23	24	25	26	27	18	19	20	21	22	23	24	23	24	25	26	27	28	29
23	24	25	26	27	28	29	28	29	30	31				25	26	27	28	29	30		30	31					

Impact on International Rail Freight


- Reduction of available capacity; possible delays due speed reduction
- Marginal residual capacity
- in the annual TT: Yes
- Extra running time max 15 Min
- Profile restrictions No

Impact of TCR 2024 at SBB Infra/BLS Netz (3)

Section Arth-Goldau – Bellinzona (Osogna-Cresciano)



State of play : 01.10.2024
Disclaimer see front page

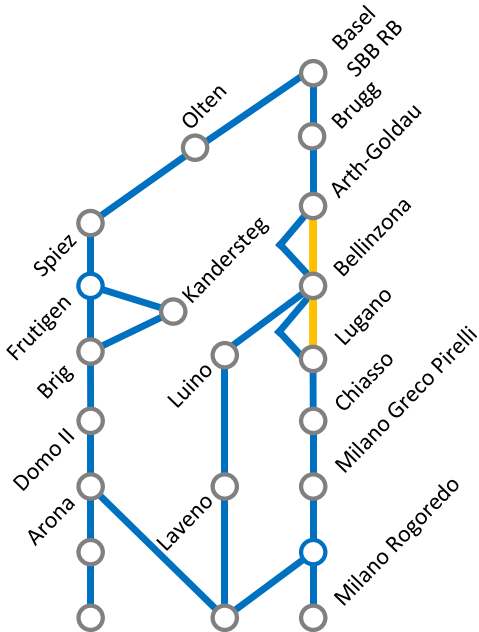

Major Capacity Restriction

- Section: Arth-Goldau – Bellinzona (Osogna-C.)
- Type: partly single-track ops / speed reduction
- Type of Works: track renewal
- Period: From 10.08.2024 to 30.08.2024

2024 Calendar

Single track operation Total closure

January							February							March							April						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7								1	2	3					1	2	3	4	5	6	7
8	9	10	11	12	13	14	5	6	7	8	9	10	11	4	5	6	7	8	9	10	8	9	10	11	12	13	14
15	16	17	18	19	20	21	12	13	14	15	16	17	18	11	12	13	14	15	16	17	15	16	17	18	19	20	21
22	23	24	25	26	27	28	19	20	21	22	23	24	25	18	19	20	21	22	23	24	22	23	24	25	26	27	28
29	30	31					26	27	28	29				25	26	27	28	29	30	31	29	30					

May							June							July							August						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
			1	2	3	4						1	2	1	2	3	4	5	6	7	5	6	7	8	9	10	11
6	7	8	9	10	11	12	3	4	5	6	7	8	9	8	9	10	11	12	13	14	12	13	14	15	16	17	18
13	14	15	16	17	18	19	10	11	12	13	14	15	16	15	16	17	18	19	20	21	12	13	14	15	16	17	18
20	21	22	23	24	25	26	17	18	19	20	21	22	23	22	23	24	25	26	27	28	19	20	21	22	23	24	25
27	28	29	30	31			24	25	26	27	28	29	30	29	30	31					26	27	28	29	30	31	

September							October							November							December						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
						1		1	2	3	4	5	6		1	2	3				2	3	4	5	6	7	8
2	3	4	5	6	7	8	7	8	9	10	11	12	13	4	5	6	7	8	9	10	9	10	11	12	13	14	15
9	10	11	12	13	14	15	14	15	16	17	18	19	20	11	12	13	14	15	16	17	16	17	18	19	20	21	22
16	17	18	19	20	21	22	21	22	23	24	25	26	27	18	19	20	21	22	23	24	23	24	25	26	27	28	29
23	24	25	26	27	28	29	28	29	30	31				25	26	27	28	29	30		30	31					
30																											

Impact on International Rail Freight


- Reduction of available capacity; delays due speed reduction
- Marginal residual capacity
- in the annual TT: Yes
- Extra running time max 30 Min
- Profile restrictions No

Impact of TCR 2024 at SBB Infra/BLS Netz (4)

Section Basel SBB RB – Brugg



State of play : 01.10.2024
Disclaimer see front page

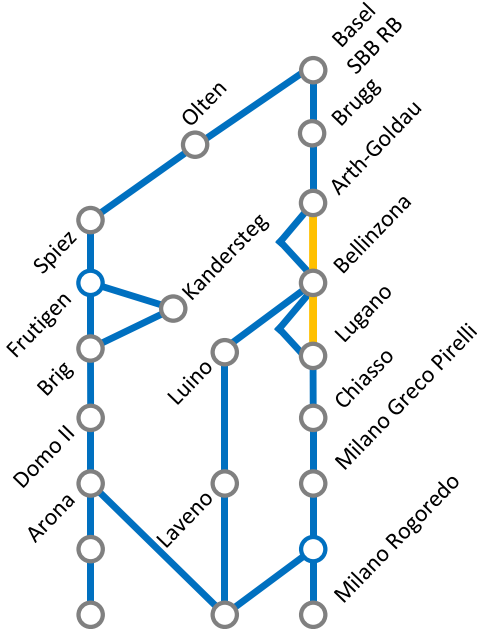

Major Capacity Restriction

- Section: Basel SBB RB – Brugg
- Type: single-track operation
- Type of Works: track renewal
- Period: From 22.03.2024 to 24.06.2024
- Period: From 11.08.2024 to 08.11.2024

2024 Calendar

Single track operation Total closure

January							February							March							April						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7															1	2	3	4	5	6	7
8	9	10	11	12	13	14	5	6	7	8	9	10	11	4	5	6	7	8	9	10	8	9	10	11	12	13	14
15	16	17	18	19	20	21	12	13	14	15	16	17	18	11	12	13	14	15	16	17	15	16	17	18	19	20	21
22	23	24	25	26	27	28	19	20	21	22	23	24	25	18	19	20	21	22	23	24	22	23	24	25	26	27	28
29	30	31					26	27	28	29				25	26	27	28	29	30	31	29	30					

May							June							July							August							
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	
		1	2	3	4	5						1	2	1	2	3	4	5	6	7					1	2	3	4
6	7	8	9	10	11	12	3	4	5	6	7	8	9	8	9	10	11	12	13	14	5	6	7	8	9	10	11	
13	14	15	16	17	18	19	10	11	12	13	14	15	16	15	16	17	18	19	20	21	12	13	14	15	16	17	18	
20	21	22	23	24	25	26	17	18	19	20	21	22	23	22	23	24	25	26	27	28	19	20	21	22	23	24	25	
27	28	29	30	31			24	25	26	27	28	29	30	29	30	31					26	27	28	29	30	31		

September							October							November							December						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
						1						1	2	3	4	5	6	7	8	9	2	3	4	5	6	7	8
2	3	4	5	6	7	8	7	8	9	10	11	12	13	4	5	6	7	8	9	10	9	10	11	12	13	14	15
9	10	11	12	13	14	15	14	15	16	17	18	19	20	11	12	13	14	15	16	17	16	17	18	19	20	21	22
16	17	18	19	20	21	22	21	22	23	24	25	26	27	18	19	20	21	22	23	24	23	24	25	26	27	28	29
23	24	25	26	27	28	29	28	29	30	31				25	26	27	28	29	30		30	31					
30																											

Impact on International Rail Freight


- Reduction of available capacity; delays due speed reduction
- Marginal residual capacity
- in the annual TT: No
- Profile restrictions No

Impact of TCR 2024 at RFI

Section Milano - Domodossola



State of play : 01.10.2024
Disclaimer see front page

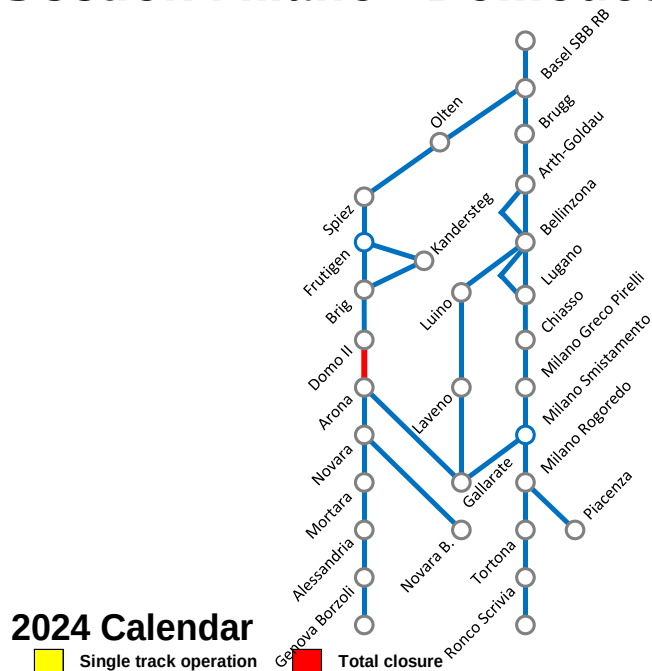

2024 Calendar

Single track operation
Total closure

January						
Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7
8	9	10	11	12	13	14
15	16	17	18	19	20	21
22	23	24	25	26	27	28
29	30	31				

February						
Mo	Tu	We	Th	Fr	Sa	Su
			1	2	3	4
5	6	7	8	9	10	11
12	13	14	15	16	17	18
19	20	21	22	23	24	25
26	27	28	29			

March						
Mo	Tu	We	Th	Fr	Sa	Su
				1	2	3
4	5	6	7	8	9	10
11	12	13	14	15	16	17
18	19	20	21	22	23	24
25	26	27	28	29	30	31

April						
Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7
8	9	10	11	12	13	14
15	16	17	18	19	20	21
22	23	24	25	26	27	28
29	30					

May						
Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	5
6	7	8	9	10	11	12
13	14	15	16	17	18	19
20	21	22	23	24	25	26
27	28	29	30	31		

June						
Mo	Tu	We	Th	Fr	Sa	Su
				1	2	
3	4	5	6	7	8	9
10	11	12	13	14	15	16
17	18	19	20	21	22	23
24	25	26	27	28	29	30

July						
Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7
8	9	10	11	12	13	14
15	16	17	18	19	20	21
22	23	24	25	26	27	28
29	30	31				

August						
Mo	Tu	We	Th	Fr	Sa	Su
				1	2	3
4	5	6	7	8	9	10
11	12	13	14	15	16	17
18	19	20	21	22	23	24
25	26	27	28	29	30	31

September						
Mo	Tu	We	Th	Fr	Sa	Su
						1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	29
30						

October						
Mo	Tu	We	Th	Fr	Sa	Su
	1	2	3	4	5	6
7	8	9	10	11	12	13
14	15	16	17	18	19	20
21	22	23	24	25	26	27
28	29	30	31			

November						
Mo	Tu	We	Th	Fr	Sa	Su
				1	2	3
4	5	6	7	8	9	10
11	12	13	14	15	16	17
18	19	20	21	22	23	24
25	26	27	28	29	30	

December						
Mo	Tu	We	Th	Fr	Sa	Su
						1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	29
30	31					

Major Capacity Restriction

- Section: Arona - Verbania
- Typ: Total Closure of 90 days
- Period: 09.06.2024 - 08.09.2024
- Type of works: Gauge enhancement - P/C 80

Impact on International Rail Freight


- Deviations: Yes
- Restrictions in train parameters: no
- Restrictions in container profile: no
- In annual timetable: Yes

Impact of TCR 2024 at RFI

Section Milano - Domodossola



State of play : 01.10.2024
Disclaimer see front page

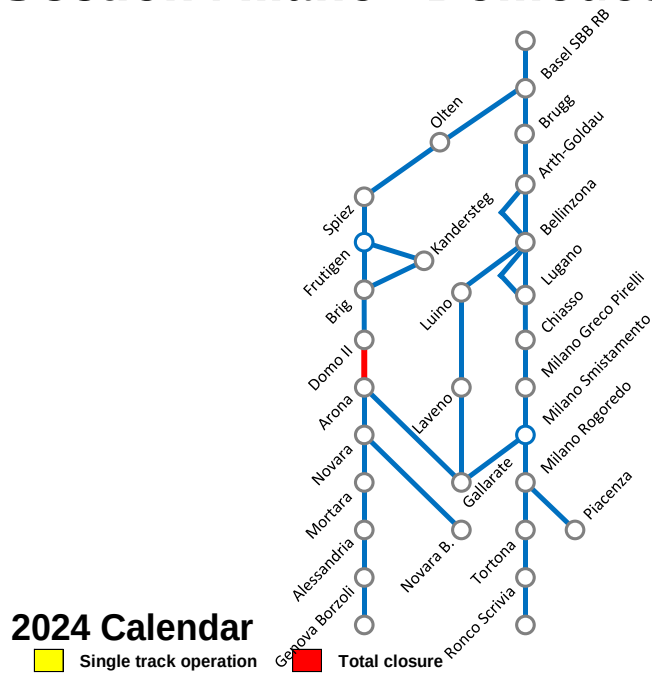

2024 Calendar

Single track operation Total closure

January						
Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7
8	9	10	11	12	13	14
15	16	17	18	19	20	21
22	23	24	25	26	27	28
29	30	31				

February						
Mo	Tu	We	Th	Fr	Sa	Su
			1	2	3	4
5	6	7	8	9	10	11
12	13	14	15	16	17	18
19	20	21	22	23	24	25
26	27	28	29			

March						
Mo	Tu	We	Th	Fr	Sa	Su
				1	2	3
4	5	6	7	8	9	10
11	12	13	14	15	16	17
18	19	20	21	22	23	24
25	26	27	28	29	30	31

April						
Mo	Tu	We	Th	Fr	Sa	Su
	1	2	3	4	5	6
7	8	9	10	11	12	13
14	15	16	17	18	19	20
21	22	23	24	25	26	27
28	29	30				

May						
Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	5
6	7	8	9	10	11	12
13	14	15	16	17	18	19
20	21	22	23	24	25	26
27	28	29	30	31		

June						
Mo	Tu	We	Th	Fr	Sa	Su
				1	2	
3	4	5	6	7	8	9
10	11	12	13	14	15	16
17	18	19	20	21	22	23
24	25	26	27	28	29	30

July						
Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7
8	9	10	11	12	13	14
15	16	17	18	19	20	21
22	23	24	25	26	27	28
29	30	31				

August						
Mo	Tu	We	Th	Fr	Sa	Su
				1	2	3
4	5	6	7	8	9	10
11	12	13	14	15	16	17
18	19	20	21	22	23	24
25	26	27	28	29	30	31

September						
Mo	Tu	We	Th	Fr	Sa	Su
						1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	29
30						

October						
Mo	Tu	We	Th	Fr	Sa	Su
	1	2	3	4	5	6
7	8	9	10	11	12	13
14	15	16	17	18	19	20
21	22	23	24	25	26	27
28	29	30	31			

November						
Mo	Tu	We	Th	Fr	Sa	Su
				1	2	3
4	5	6	7	8	9	10
11	12	13	14	15	16	17
18	19	20	21	22	23	24
25	26	27	28	29	30	

December						
Mo	Tu	We	Th	Fr	Sa	Su
						1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	29
30	31					

Major Capacity Restriction

- Section: Arona - Sesto Calende
- Typ: Odd Track Closure of 90 days (in shadow to Arona - Verbania total closure)
- Period: 09.06.2024 - 08.09.2024
- Type of works: Completion of metal girder work in Sesto Calende

Impact on International Rail Freight


- Deviations: Yes - the same train measures taking into consideration for Arona - Verbania total closure
- Restrictions in train parameters: no
- Restrictions in container profile: no
- In annual timetable: No

Impact of TCR 2024 at RFI

Section Domodossola - Iselle



State of play : 01.10.2024
Disclaimer see front page

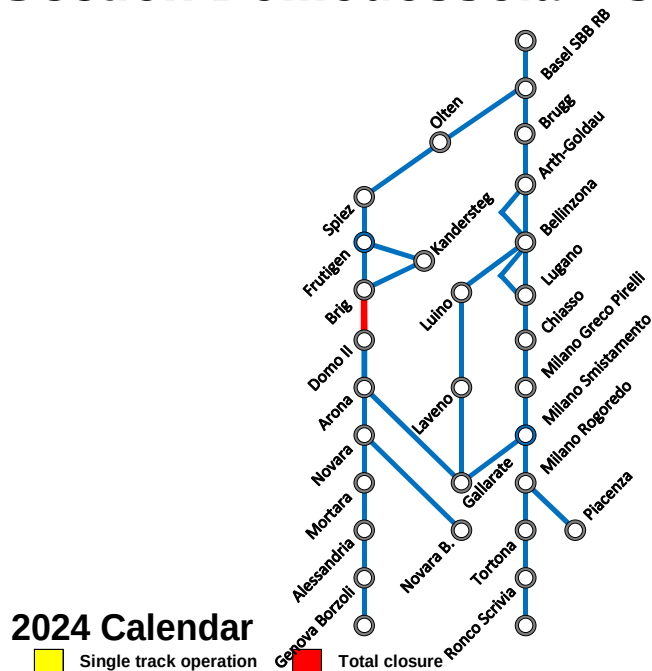

2024 Calendar

Single track operation
Total closure

January						
Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7
8	9	10	11	12	13	14
15	16	17	18	19	20	21
22	23	24	25	26	27	28
29	30	31				

February						
Mo	Tu	We	Th	Fr	Sa	Su
			1	2	3	4
5	6	7	8	9	10	11
12	13	14	15	16	17	18
19	20	21	22	23	24	25
26	27	28	29			

March						
Mo	Tu	We	Th	Fr	Sa	Su
				1	2	3
4	5	6	7	8	9	10
11	12	13	14	15	16	17
18	19	20	21	22	23	24
25	26	27	28	29	30	31

April						
Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7
8	9	10	11	12	13	14
15	16	17	18	19	20	21
22	23	24	25	26	27	28
29	30					

May						
Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	5
6	7	8	9	10	11	12
13	14	15	16	17	18	19
20	21	22	23	24	25	26
27	28	29	30	31		

June						
Mo	Tu	We	Th	Fr	Sa	Su
				1	2	
3	4	5	6	7	8	9
10	11	12	13	14	15	16
17	18	19	20	21	22	23
24	25	26	27	28	29	30

July						
Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7
8	9	10	11	12	13	14
15	16	17	18	19	20	21
22	23	24	25	26	27	28
29	30	31				

August						
Mo	Tu	We	Th	Fr	Sa	Su
			1	2	3	4
5	6	7	8	9	10	11
12	13	14	15	16	17	18
19	20	21	22	23	24	25
26	27	28	29	30	31	

September						
Mo	Tu	We	Th	Fr	Sa	Su
						1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	29
30						

October						
Mo	Tu	We	Th	Fr	Sa	Su
	1	2	3	4	5	6
7	8	9	10	11	12	13
14	15	16	17	18	19	20
21	22	23	24	25	26	27
28	29	30	31			

November						
Mo	Tu	We	Th	Fr	Sa	Su
				1	2	3
4	5	6	7	8	9	10
11	12	13	14	15	16	17
18	19	20	21	22	23	24
25	26	27	28	29	30	

December						
Mo	Tu	We	Th	Fr	Sa	Su
						1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	29
30	31					

Major Capacity Restriction

- Section: Domodossola - Iselle
- Typ: Total Closure of 21 days
- Period: 09.08.2024 - 30.08.2024
- Type of works: Extraordinary maintenance of Boldrini bridge

Impact on International Rail Freight


- Deviations: Yes - train measures defined by SBB-Infrastruktur
- Restrictions in train parameters: no
- Restrictions in container profile: no
- In annual timetable: No

Impact of TCR 2024 at RFI

Section Luino - Pino Tronzano



State of play : 01.10.2024
Disclaimer see front page

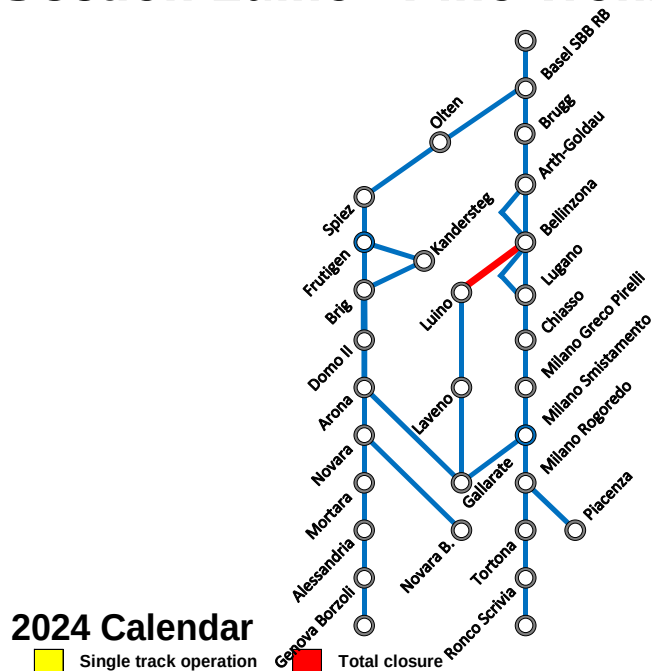

2024 Calendar

Single track operation Total closure

January						
Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7
8	9	10	11	12	13	14
15	16	17	18	19	20	21
22	23	24	25	26	27	28
29	30	31				

February						
Mo	Tu	We	Th	Fr	Sa	Su
			1	2	3	4
5	6	7	8	9	10	11
12	13	14	15	16	17	18
19	20	21	22	23	24	25
26	27	28	29			

March						
Mo	Tu	We	Th	Fr	Sa	Su
				1	2	3
4	5	6	7	8	9	10
11	12	13	14	15	16	17
18	19	20	21	22	23	24
25	26	27	28	29	30	31

April						
Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7
8	9	10	11	12	13	14
15	16	17	18	19	20	21
22	23	24	25	26	27	28
29	30					

May						
Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	5
6	7	8	9	10	11	12
13	14	15	16	17	18	19
20	21	22	23	24	25	26
27	28	29	30	31		

June						
Mo	Tu	We	Th	Fr	Sa	Su
				1	2	
3	4	5	6	7	8	9
10	11	12	13	14	15	16
17	18	19	20	21	22	23
24	25	26	27	28	29	30

July						
Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7
8	9	10	11	12	13	14
15	16	17	18	19	20	21
22	23	24	25	26	27	28
29	30	31				

August						
Mo	Tu	We	Th	Fr	Sa	Su
			1	2	3	4
5	6	7	8	9	10	11
12	13	14	15	16	17	18
19	20	21	22	23	24	25
26	27	28	29	30	31	

September						
Mo	Tu	We	Th	Fr	Sa	Su
						1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	29
30						

October						
Mo	Tu	We	Th	Fr	Sa	Su
	1	2	3	4	5	6
7	8	9	10	11	12	13
14	15	16	17	18	19	20
21	22	23	24	25	26	27
28	29	30	31			

November						
Mo	Tu	We	Th	Fr	Sa	Su
				1	2	3
4	5	6	7	8	9	10
11	12	13	14	15	16	17
18	19	20	21	22	23	24
25	26	27	28	29	30	

December						
Mo	Tu	We	Th	Fr	Sa	Su
						1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	29
30	31					

Major Capacity Restriction

- Section: Luino - Pino Tronzano
- Typ: Total Closure of 21 days
- Period: 07.01.2024 - 28.01.2024
- Type of works: Extraordinary maintenance of tunnels and bridges

Impact on International Rail Freight


- Deviations: Yes - train measures defined by SBB-Infrastruktur
- Restrictions in train parameters: no
- Restrictions in container profile: no
- In annual timetable: No

Impact of TCR 2024 at RFI

Section Luino - Gallarate



State of play : 01.10.2024
Disclaimer see front page

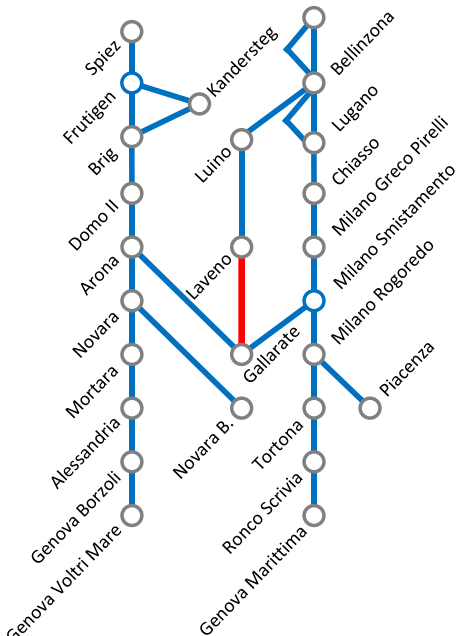

Major Capacity Restriction

- Section: Laveno - Ternate
- Typ: Total Closure of 7 days
- Period: 09.09.2024 - 15.09.2024
- Type of works: hydraulic crossing of Laveno station

2024 Calendar

Single track operation Total closure

January							February							March							April						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7				1	2	3	4					1	2	3	1	2	3	4	5	6	7
8	9	10	11	12	13	14	5	6	7	8	9	10	11	4	5	6	7	8	9	10	8	9	10	11	12	13	14
15	16	17	18	19	20	21	12	13	14	15	16	17	18	11	12	13	14	15	16	17	15	16	17	18	19	20	21
22	23	24	25	26	27	28	19	20	21	22	23	24	25	18	19	20	21	22	23	24	22	23	24	25	26	27	28
29	30	31					26	27	28	29				25	26	27	28	29	30	31	29	30					

May							June							July							August						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	5						1	2					1	2	3	4						
6	7	8	9	10	11	12	3	4	5	6	7	8	9	8	9	10	11	12	13	14	5	6	7	8	9	10	11
13	14	15	16	17	18	19	10	11	12	13	14	15	16	15	16	17	18	19	20	21	12	13	14	15	16	17	18
20	21	22	23	24	25	26	17	18	19	20	21	22	23	22	23	24	25	26	27	28	19	20	21	22	23	24	25
27	28	29	30	31			24	25	26	27	28	29	30	29	30	31					26	27	28	29	30	31	


September							October							November							December						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
						1		1	2	3	4	5	6					1	2	3						1	
2	3	4	5	6	7	8	7	8	9	10	11	12	13	4	5	6	7	8	9	10	2	3	4	5	6	7	8
9	10	11	12	13	14	15	14	15	16	17	18	19	20	11	12	13	14	15	16	17	9	10	11	12	13	14	15
16	17	18	19	20	21	22	21	22	23	24	25	26	27	18	19	20	21	22	23	24	16	17	18	19	20	21	22
23	24	25	26	27	28	29	28	29	30	31				25	26	27	28	29	30		23	24	25	26	27	28	29
30														30	31						30	31					

Impact on International Rail Freight

- Deviations: Yes
- Restrictions in train parameters: no
- Restrictions in container profile: no
- In annual timetable: no, timetables adapted 4 weeks before operation

Impact of TCR 2024 at RFI – Focus Terzo Valico project Genova

State of play : 21.12.2023
Disclaimer see front page

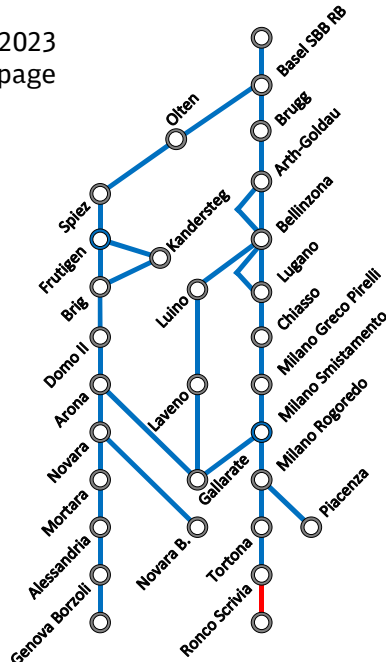

State of play : 01.10.2024
Disclaimer see front page



Major Capacity Restriction

- Section: Quadrivio Torbella – Bivio Polcevera
- Typ: Two Total Closure of the lines:
 - Quadrivio Torbella - Ventimiglia
 - Quadrivio Torbella - Genova Marittima
Bacino di San Pier d'Arena
 - Bivio Polcevera – Genova Borzoli
- Period:
 - 28.12.2023 – 07.01.2024
 - 03.08.2024 – 01.09.2024
- Type of works: III Valico project

2024 Calendar

■ Single track operation ■ Total closure

January							February							March							April							
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	
1	2	3	4	5	6	7				1	2	3	4					1	2	3		1	2	3	4	5	6	7
8	9	10	11	12	13	14	5	6	7	8	9	10	11	4	5	6	7	8	9	10	8	9	10	11	12	13	14	
15	16	17	18	19	20	21	12	13	14	15	16	17	18	11	12	13	14	15	16	17	15	16	17	18	19	20	21	
22	23	24	25	26	27	28	19	20	21	22	23	24	25	18	19	20	21	22	23	24	22	23	24	25	26	27	28	
29	30	31					26	27	28	29				25	26	27	28	29	30	31	29	30						

May							June							July							August						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
			1	2	3	4						1	2		1	2	3	4	5	6	7	5	6	7	8	9	10
6	7	8	9	10	11	12	3	4	5	6	7	8	9	8	9	10	11	12	13	14	12	13	14	15	16	17	18
13	14	15	16	17	18	19	10	11	12	13	14	15	16	15	16	17	18	19	20	21	19	20	21	22	23	24	25
20	21	22	23	24	25	26	17	18	19	20	21	22	23	22	23	24	25	26	27	28	26	27	28	29	30	31	
27	28	29	30	31			24	25	26	27	28	29	30	29	30	31											

September							October							November							December						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
						1		1	2	3	4	5	6					1	2	3						1	
2	3	4	5	6	7	8	7	8	9	10	11	12	13	4	5	6	7	8	9	10	2	3	4	5	6	7	8
9	10	11	12	13	14	15	14	15	16	17	18	19	20	11	12	13	14	15	16	17	9	10	11	12	13	14	15
16	17	18	19	20	21	22	21	22	23	24	25	26	27	18	19	20	21	22	23	24	16	17	18	19	20	21	22
23	24	25	26	27	28	29	28	29	30	31				25	26	27	28	29	30		23	24	25	26	27	28	29
30																					30	31					

Impact on International Rail Freight


- Deviations: Cancellation of the trains to Genova Marittima Bacino di San Pier d'Arena and re-routing via Ovada for trains with Genova Voltri or Ventimiglia direction (Alessandria – Genova Borzoli – PP Corvi – Genova Voltri – Ventimiglia)
- Restrictions in train parameters: Re-routing trains:
 - Alessandria – Genova Voltri: train length: 355 m – at maximum 575 m with RFI permission
 - Genova Voltri – Ventimiglia: train length: 500 m
- Restrictions in container profile: Re-routing trains:
 - Alessandria – Genova Voltri: P/C 45
 - Genova Voltri – Ventimiglia: P/C 22
- In annual timetable: Yes

Impact of TCR 2025 at Infrabel

Section Y.Berneau – Y.Oost Dr Aarschot



State of play : 01.10.2024
Disclaimer see front page

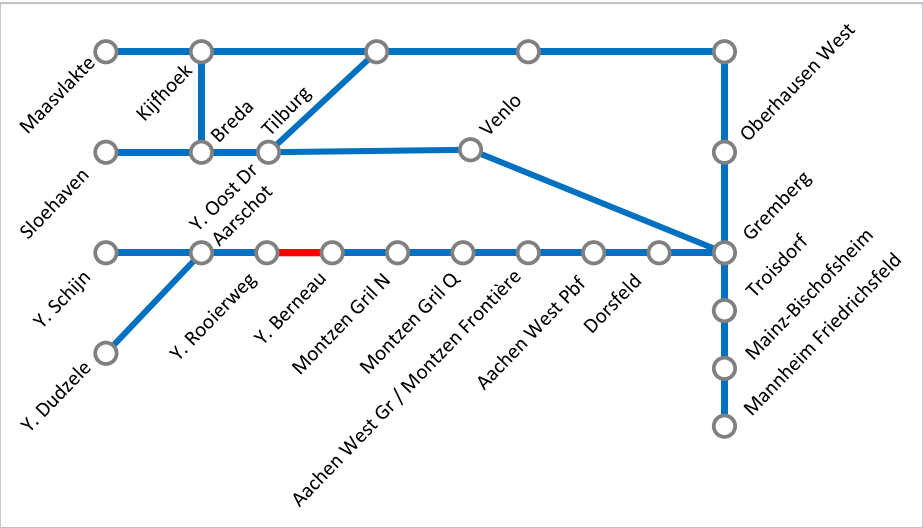

Major Capacity Restriction

- Section : Hasselt-Tongeren
- Type: Total Closure
- Period: 08.11.2025 (0:00) – 17.11.2025 (4:00)
- Type of works: Switches & level crossing renewal

2025 Calendar

Single track operation Total closure

January							February							March							April						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	5						1	2						1	2						1	2
6	7	8	9	10	11	12	3	4	5	6	7	8	9	3	4	5	6	7	8	9	7	8	9	10	11	12	13
13	14	15	16	17	18	19	10	11	12	13	14	15	16	10	11	12	13	14	15	16	14	15	16	17	18	19	20
20	21	22	23	24	25	26	17	18	19	20	21	22	23	17	18	19	20	21	22	23	21	22	23	24	25	26	27
27	28	29	30	31			24	25	26	27	28			24	25	26	27	28	29	30	28	29	30				
														31													

May							June							July							August						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
					1	2							1						1	2						1	2
5	6	7	8	9	10	11	2	3	4	5	6	7	8	7	8	9	10	11	12	13	4	5	6	7	8	9	10
12	13	14	15	16	17	18	9	10	11	12	13	14	15	14	15	16	17	18	19	20	11	12	13	14	15	16	17
19	20	21	22	23	24	25	16	17	18	19	20	21	22	21	22	23	24	25	26	27	18	19	20	21	22	23	24
26	27	28	29	30	31		23	24	25	26	27	28	29	28	29	30	31				25	26	27	28	29	30	31
							30																				

September							October							November							December						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7			1	2	3	4	5						1	2						1	2
8	9	10	11	12	13	14	6	7	8	9	10	11	12	3	4	5	6	7	8	9	8	9	10	11	12	13	14
15	16	17	18	19	20	21	13	14	15	16	17	18	19	10	11	12	13	14	15	16	15	16	17	18	19	20	21
22	23	24	25	26	27	28	20	21	22	23	24	25	26	17	18	19	20	21	22	23	22	23	24	25	26	27	28
29	30						27	28	29	30	31			24	25	26	27	28	29	30	29	30	31				

Impact on International Rail Freight


- Cancellations: No
- Deviations: Via L40-36A-36
- Estimated extra running time: tbd
- In annual timetable: No

Impact of TCR 2025 at DB InfraGO AG

Section Emmerich Border - Oberhausen Main Station



State of play : 01.10.2024
Disclaimer see front page

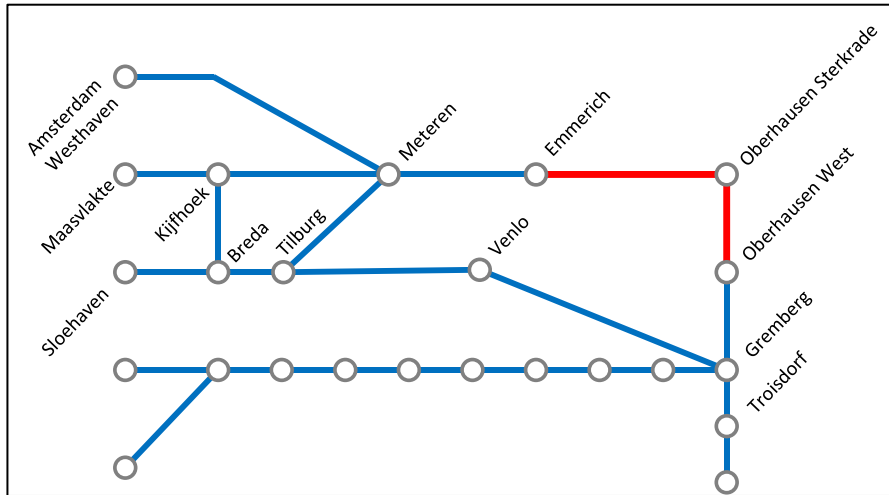

Major Capacity Restriction

- Location: Emmerich Border - Oberhausen Main Station
- Type: Total Closure, Single Track Operation
- Period: Continuous
- Type of works: Type of works: Track & Rail, Bridge, Catenary, Switch, Miscellaneous

2025 Calendar

 Single track operation Total closure

January							February							March							April						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	5						1	2							1	2						
6	7	8	9	10	11	12	3	4	5	6	7	8	9	3	4	5	6	7	8	9	7	8	9	10	11	12	13
13	14	15	16	17	18	19	10	11	12	13	14	15	16	10	11	12	13	14	15	16	14	15	16	17	18	19	20
20	21	22	23	24	25	26	17	18	19	20	21	22	23	17	18	19	20	21	22	23	21	22	23	24	25	26	27
27	28	29	30	31			24	25	26	27	28			24	25	26	27	28	29	30	28	29	30				
														31													

May							June							July							August						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
			1	2	3	4							1							1	2	3					
5	6	7	8	9	10	11	2	3	4	5	6	7	8	7	8	9	10	11	12	13	4	5	6	7	8	9	10
12	13	14	15	16	17	18	9	10	11	12	13	14	15	14	15	16	17	18	19	20	11	12	13	14	15	16	17
19	20	21	22	23	24	25	16	17	18	19	20	21	22	21	22	23	24	25	26	27	18	19	20	21	22	23	24
26	27	28	29	30	31		23	24	25	26	27	28	29	28	29	30	31				25	26	27	28	29	30	31
							30																				

September							October							November							December						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7				1	2	3	4							1	2	3	4	5	6	7	
8	9	10	11	12	13	14	6	7	8	9	10	11	12	3	4	5	6	7	8	9	8	9	10	11	12	13	14
15	16	17	18	19	20	21	13	14	15	16	17	18	19	10	11	12	13	14	15	16	15	16	17	18	19	20	21
22	23	24	25	26	27	28	20	21	22	23	24	25	26	17	18	19	20	21	22	23	22	23	24	25	26	27	28
29	30						27	28	29	30	31			24	25	26	27	28	29	30	29	30	31				

Impact on International Rail Freight


- Cancellations: Yes
- Deviations: Yes
- Estimated extra running time: Detailed information on extra running time is distributed by DB InfraGO individually for every customer for each affected train. Additionally DB InfraGO offers train path advice free of charge
- In annual timetable: Yes

Impact of TCR 2025 at DB InfraGO AG

Section Karlsruhe – Offenburg (Rhine Valley)



State of play : 01.10.2024
Disclaimer see front page

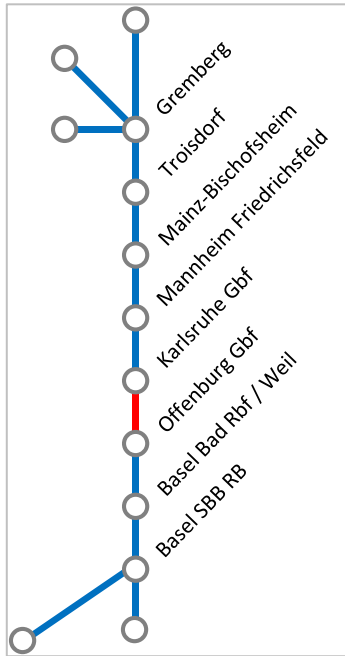

2025 Calendar

Single track operation Total closure

January							February							March							April						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	5						1	2						1	2							
6	7	8	9	10	11	12	3	4	5	6	7	8	9	3	4	5	6	7	8	9	7	8	9	10	11	12	13
13	14	15	16	17	18	19	10	11	12	13	14	15	16	10	11	12	13	14	15	16	14	15	16	17	18	19	20
20	21	22	23	24	25	26	17	18	19	20	21	22	23	17	18	19	20	21	22	23	21	22	23	24	25	26	27
27	28	29	30	31			24	25	26	27	28			24	25	26	27	28	29	30	28	29	30				
														31													
May							June							July							August						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
			1	2	3	4							1		1	2	3	4	5	6					1	2	3
5	6	7	8	9	10	11	2	3	4	5	6	7	8	7	8	9	10	11	12	13	4	5	6	7	8	9	10
12	13	14	15	16	17	18	9	10	11	12	13	14	15	14	15	16	17	18	19	20	11	12	13	14	15	16	17
19	20	21	22	23	24	25	16	17	18	19	20	21	22	21	22	23	24	25	26	27	18	19	20	21	22	23	24
26	27	28	29	30	31		23	24	25	26	27	28	29	28	29	30	31				25	26	27	28	29	30	31
							30																				
September							October							November							December						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7		1	2	3	4	5			1	2	3	4	5	6	1	2	3	4	5	6	7
8	9	10	11	12	13	14	6	7	8	9	10	11	12	3	4	5	6	7	8	9	8	9	10	11	12	13	14
15	16	17	18	19	20	21	13	14	15	16	17	18	19	10	11	12	13	14	15	16	15	16	17	18	19	20	21
22	23	24	25	26	27	28	20	21	22	23	24	25	26	17	18	19	20	21	22	23	22	23	24	25	26	27	28
29	30						27	28	29	30	31			24	25	26	27	28	29	30	29	30	31				

Major Capacity Restriction

- Section: Orschweier Nord - Windschläg (Total closure Offenburg Gbf/Pbf)
- Typ: Total Closure
- Period: April 2025
- Type of works: Signalling

Impact on International Rail Freight


- Cancellations: Yes
- Deviations: Yes, via Gäubahn or Brenner
- Estimated extra running time: Detailed information on extra running time is distributed by DB InfraGO individually for every customer for each affected train. Additionally DB InfraGO offers train path advice free of charge
- In annual timetable: No

Impact of TCR 2025 at DB InfraGO AG

Section Offenburg – Haltingen (Rhine Valley)



State of play : 01.10.2024
Disclaimer see front page

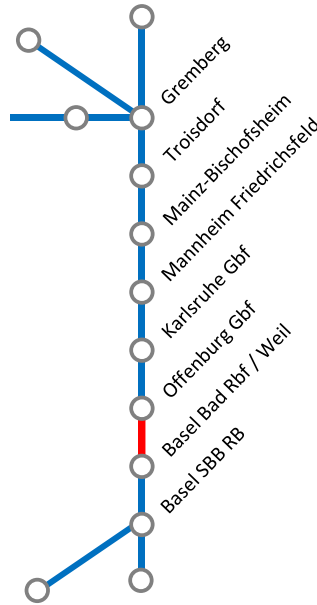

Major Capacity Restriction

- First phase (Jan-Feb): Single track operation Schliengen Nord – Heitersheim (VzG 4000)
- Second phase (Apr-Jun): Total closure of Katzenberg tunnel (VzG 4280) + Single track operation Rheinweiler-Müllheim (VzG 4000)
- Type of works: Catenary, Track & Rail, Miscellaneous, Commissioning of new tracks

2025 Calendar

 Single track operation Total closure

January							February							March							April						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	5						1	2									1	2	3	4	5	6
6	7	8	9	10	11	12	3	4	5	6	7	8	9	3	4	5	6	7	8	9	7	8	9	10	11	12	13
13	14	15	16	17	18	19	10	11	12	13	14	15	16	10	11	12	13	14	15	16	14	15	16	17	18	19	20
20	21	22	23	24	25	26	17	18	19	20	21	22	23	17	18	19	20	21	22	23	21	22	23	24	25	26	27
27	28	29	30	31			24	25	26	27	28			24	25	26	27	28	29	30	28	29	30				
														31													

May							June							July							August						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
			1	2	3	4						1	2		1	2	3	4	5	6					1	2	3
5	6	7	8	9	10	11	2	3	4	5	6	7	8	7	8	9	10	11	12	13	4	5	6	7	8	9	10
12	13	14	15	16	17	18	9	10	11	12	13	14	15	14	15	16	17	18	19	20	11	12	13	14	15	16	17
19	20	21	22	23	24	25	16	17	18	19	20	21	22	21	22	23	24	25	26	27	18	19	20	21	22	23	24
26	27	28	29	30	31		23	24	25	26	27	28	29	28	29	30	31				25	26	27	28	29	30	31
							30																				

September							October							November							December						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7		1	2	3	4	5			1	2	3	4	5	6	1	2	3	4	5	6	7
8	9	10	11	12	13	14	6	7	8	9	10	11	12	3	4	5	6	7	8	9	8	9	10	11	12	13	14
15	16	17	18	19	20	21	13	14	15	16	17	18	19	10	11	12	13	14	15	16	15	16	17	18	19	20	21
22	23	24	25	26	27	28	20	21	22	23	24	25	26	17	18	19	20	21	22	23	22	23	24	25	26	27	28
29	30						27	28	29	30	31			24	25	26	27	28	29	30	29	30	31				

Impact on International Rail Freight

- Cancellations: Yes
- Deviations: Yes, via Gäubahn
- Estimated extra running time: Detailed information on extra running time is distributed by DB InfraGO individually for every customer for each affected train. Additionally DB InfraGO offers train path advice free of charge
- In annual timetable: No

Impact of TCR 2025 at DB InfraGO AG

Section Offenburg – Haltingen (Rhine Valley)



State of play : 01.10.2024
Disclaimer see front page



Major Capacity Restriction

- First phase (Jan-Feb): Single track operation Schliengen Nord – Heitersheim (VzG 4000)
- Second phase (Apr-Jun): Total closure of Katzenberg tunnel (VzG 4280) + Single track operation Rheinweiler-Müllheim (VzG 4000)
- Type of works: Catenary, Track & Rail, Miscellaneous, Commissioning of new tracks

2025 Calendar

 Single track operation Total closure

January							February							March							April						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	5						1	2									1	2	3	4	5	6
6	7	8	9	10	11	12								3	4	5	6	7	8	9	10	11	12	13	14	15	16
13	14	15	16	17	18	19	10	11	12	13	14	15	16	10	11	12	13	14	15	16	17	18	19	20	21	22	23
20	21	22	23	24	25	26	17	18	19	20	21	22	23	17	18	19	20	21	22	23	24	25	26	27	28	29	30
27	28	29	30	31			24	25	26	27	28			24	25	26	27	28	29	30							
														31													

May							June							July							August						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
			1	2	3	4							1		1	2	3	4	5	6							
5	6	7	8	9	10	11	2	3	4	5	6	7	8	7	8	9	10	11	12	13	11	12	13	14	15	16	17
12	13	14	15	16	17	18	9	10	11	12	13	14	15	14	15	16	17	18	19	20	18	19	20	21	22	23	24
19	20	21	22	23	24	25	16	17	18	19	20	21	22	21	22	23	24	25	26	27	25	26	27	28	29	30	31
26	27	28	29	30	31		23	24	25	26	27	28	29	28	29	30	31										
							30																				

September							October							November							December						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7									1	2	3	4	5	6							
8	9	10	11	12	13	14	6	7	8	9	10	11	12	3	4	5	6	7	8	9	8	9	10	11	12	13	14
15	16	17	18	19	20	21	13	14	15	16	17	18	19	10	11	12	13	14	15	16	15	16	17	18	19	20	21
22	23	24	25	26	27	28	20	21	22	23	24	25	26	17	18	19	20	21	22	23	22	23	24	25	26	27	28
29	30						27	28	29	30	31			24	25	26	27	28	29	30	29	30	31				

Impact on International Rail Freight


- Cancellations: Yes
- Deviations: Yes, via Gäubahn
- Estimated extra running time: Detailed information on extra running time is distributed by DB InfraGO individually for every customer for each affected train. Additionally DB InfraGO offers train path advice free of charge
- In annual timetable: No

Impact of TCR 2025 at SBB Infra (1)

Section Arth-Goldau - Bellinzona (Gotthard base tunnel)



State of play : 01.10.2024
Disclaimer see front page

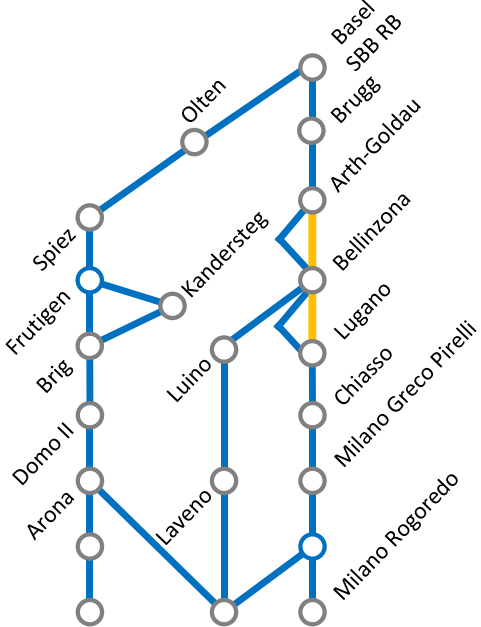

Major Capacity Restriction

- Location: Gotthard Base Tunnel
- Type: Single Track Operation
- Period:12.01.2025 - 25.01.2025
- Type of works: maintenance

2025 Calendar

 Single track operation Total closure

January							February							March							April						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	5					1	2							1	2		1	2	3	4	5	6
6	7	8	9	10	11	12	3	4	5	6	7	8	9	3	4	5	6	7	8	9	7	8	9	10	11	12	13
13	14	15	16	17	18	19	10	11	12	13	14	15	16	10	11	12	13	14	15	16	14	15	16	17	18	19	20
20	21	22	23	24	25	26	17	18	19	20	21	22	23	17	18	19	20	21	22	23	21	22	23	24	25	26	27
27	28	29	30	31			24	25	26	27	28			24	25	26	27	28	29	30	28	29	30				
														31													

May							June							July							August						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
				1	2	3							1							1		1	2	3			
5	6	7	8	9	10	11	2	3	4	5	6	7	8	7	8	9	10	11	12	13	4	5	6	7	8	9	10
12	13	14	15	16	17	18	9	10	11	12	13	14	15	14	15	16	17	18	19	20	11	12	13	14	15	16	17
19	20	21	22	23	24	25	16	17	18	19	20	21	22	21	22	23	24	25	26	27	18	19	20	21	22	23	24
26	27	28	29	30	31		23	24	25	26	27	28	29	28	29	30	31				25	26	27	28	29	30	31
							30																				

September							October							November							December						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7			1	2	3	4	5						1	2	1	2	3	4	5	6	7
8	9	10	11	12	13	14	6	7	8	9	10	11	12	3	4	5	6	7	8	9	8	9	10	11	12	13	14
15	16	17	18	19	20	21	13	14	15	16	17	18	19	10	11	12	13	14	15	16	15	16	17	18	19	20	21
22	23	24	25	26	27	28	20	21	22	23	24	25	26	17	18	19	20	21	22	23	22	23	24	25	26	27	28
29	30						27	28	29	30	31			24	25	26	27	28	29	30	29	30	31				

Impact on International Rail Freight


- Capacity reduction by 1/3
- No deviations planned
- Estimated extra running time: max 30 mins
- In annual timetable: no

Impact of TCR 2025 at SBB Infra (2)

Section Bellinzona - Chiasso



State of play : 01.10.2024
Disclaimer see front page

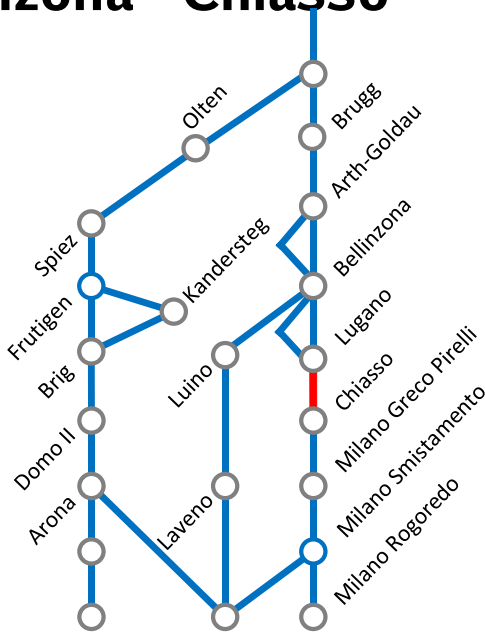

Major Capacity Restriction

- Location: Lugano / Lugano-Melide
- Type: Station track closure / single track operation
- Period: 20.06.2025 - 01.09.2025
- Type of works: construction of underpass/track renewal

2025 Calendar

Single track operation Total closure

January							February							March							April						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	5					1	2							1	2							
6	7	8	9	10	11	12	3	4	5	6	7	8	9	3	4	5	6	7	8	9	7	8	9	10	11	12	13
13	14	15	16	17	18	19	10	11	12	13	14	15	16	10	11	12	13	14	15	16	14	15	16	17	18	19	20
20	21	22	23	24	25	26	17	18	19	20	21	22	23	17	18	19	20	21	22	23	21	22	23	24	25	26	27
27	28	29	30	31			24	25	26	27	28			24	25	26	27	28	29	30	28	29	30				
														31													

May							June							July							August						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
				1	2	3							1							1							
5	6	7	8	9	10	11	2	3	4	5	6	7	8	7	8	9	10	11	12	13	4	5	6	7	8	9	10
12	13	14	15	16	17	18	9	10	11	12	13	14	15	14	15	16	17	18	19	20	11	12	13	14	15	16	17
19	20	21	22	23	24	25	16	17	18	19	20	21	22	21	22	23	24	25	26	27	18	19	20	21	22	23	24
26	27	28	29	30	31		23	24	25	26	27	28	29	28	29	30	31				25	26	27	28	29	30	31
							30																				

September							October							November							December						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7			1	2	3	4	5						1	2	1	2	3	4	5	6	7
8	9	10	11	12	13	14	6	7	8	9	10	11	12	3	4	5	6	7	8	9	8	9	10	11	12	13	14
15	16	17	18	19	20	21	13	14	15	16	17	18	19	10	11	12	13	14	15	16	15	16	17	18	19	20	21
22	23	24	25	26	27	28	20	21	22	23	24	25	26	17	18	19	20	21	22	23	22	23	24	25	26	27	28
29	30						27	28	29	30	31			24	25	26	27	28	29	30	29	30	31				

Impact on International Rail Freight


- Capacity reduction by 1/3
- No deviations planned
- Estimated extra running time: max 30 mins
- In annual timetable: no

Impact of TCR 2025 at SBB Infra (3)

Section Basel RB - Spiez



State of play : 01.10.2024
Disclaimer see front page

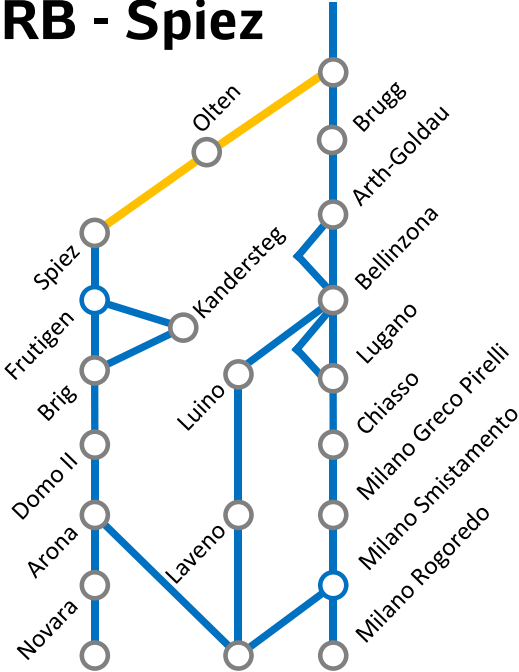

Major Capacity Restriction

- Location: Uttigen-Thun
- Type: Single Track Operation
- Period:03.06.2025 – 23.06.2025
- Type of works: track renewal

2025 Calendar

Single track operation Total closure

January							February							March							April						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	5					1	2							1	2		1	2	3	4	5	6
6	7	8	9	10	11	12	3	4	5	6	7	8	9	3	4	5	6	7	8	9	7	8	9	10	11	12	13
13	14	15	16	17	18	19	10	11	12	13	14	15	16	10	11	12	13	14	15	16	14	15	16	17	18	19	20
20	21	22	23	24	25	26	17	18	19	20	21	22	23	17	18	19	20	21	22	23	21	22	23	24	25	26	27
27	28	29	30	31			24	25	26	27	28			24	25	26	27	28	29	30	28	29	30				
														31													

May							June							July							August						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
				1	2	3	2	3	4	5	6	7	8	1	2	3	4	5	6	7	4	5	6	7	8	9	10
5	6	7	8	9	10	11	9	10	11	12	13	14	15	7	8	9	10	11	12	13	11	12	13	14	15	16	17
12	13	14	15	16	17	18	16	17	18	19	20	21	22	14	15	16	17	18	19	20	18	19	20	21	22	23	24
19	20	21	22	23	24	25	23	24	25	26	27	28	29	21	22	23	24	25	26	27	25	26	27	28	29	30	31
26	27	28	29	30	31		30							28	29	30	31										

September							October							November							December						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7	6	7	8	9	10	11	12	3	4	5	6	7	8	9	1	2	3	4	5	6	7
8	9	10	11	12	13	14	13	14	15	16	17	18	19	10	11	12	13	14	15	16	8	9	10	11	12	13	14
15	16	17	18	19	20	21	20	21	22	23	24	25	26	17	18	19	20	21	22	23	15	16	17	18	19	20	21
22	23	24	25	26	27	28	27	28	29	30	31			24	25	26	27	28	29	30	22	23	24	25	26	27	28
29	30													24	25	26	27	28	29	30	29	30	31				

Impact on International Rail Freight


- Capacity reduction by 1/3
- In the shadow of major projects in Germany and Italy
- Estimated extra running time: max 30 mins
- In annual timetable: no

Impact of TCR 2025 at SBB Infra (4)

Section Spiez-Domodossola



State of play : 01.10.2024
Disclaimer see front page

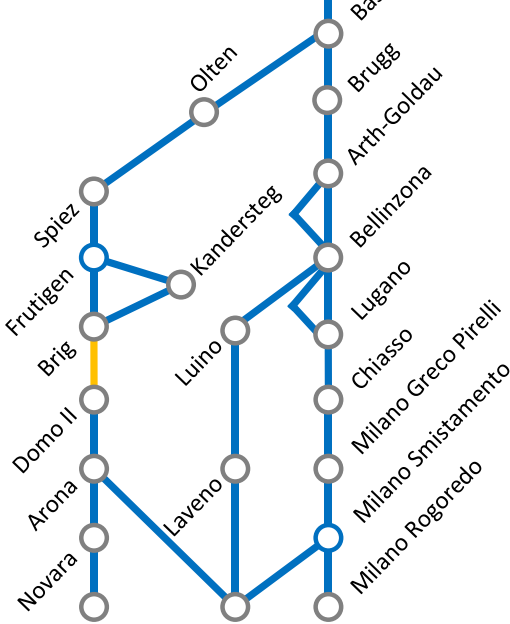

Major Capacity Restriction

- Location: Simplon tunnel
- Type: Single Track Operation (1/4 sections)
- Period:03.02.2025 – 27.07.2025
- Type of works: track and tunnel vault renovation

2025 Calendar

Single track operation Total closure

January							February							March							April						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	5						1	2						1	2		1	2	3	4	5	6
6	7	8	9	10	11	12	3	4	5	6	7	8	9	3	4	5	6	7	8	9	7	8	9	10	11	12	13
13	14	15	16	17	18	19	10	11	12	13	14	15	16	10	11	12	13	14	15	16	14	15	16	17	18	19	20
20	21	22	23	24	25	26	17	18	19	20	21	22	23	17	18	19	20	21	22	23	21	22	23	24	25	26	27
27	28	29	30	31			24	25	26	27	28			24	25	26	27	28	29	30	28	29	30				
														31													

May							June							July							August						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
				1	2	3	2	3	4	5	6	7	8	1	2	3	4	5	6		1	2	3	4	5	6	
5	6	7	8	9	10	11	9	10	11	12	13	14	15	7	8	9	10	11	12	13	4	5	6	7	8	9	10
12	13	14	15	16	17	18	16	17	18	19	20	21	22	14	15	16	17	18	19	20	11	12	13	14	15	16	17
19	20	21	22	23	24	25	23	24	25	26	27	28	29	21	22	23	24	25	26	27	18	19	20	21	22	23	24
26	27	28	29	30	31		30							28	29	30	31				25	26	27	28	29	30	31


September							October							November							December						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7	6	7	8	9	10	11	12	3	4	5	6	7	8	9	1	2	3	4	5	6	7
8	9	10	11	12	13	14	13	14	15	16	17	18	19	10	11	12	13	14	15	16	8	9	10	11	12	13	14
15	16	17	18	19	20	21	20	21	22	23	24	25	26	17	18	19	20	21	22	23	15	16	17	18	19	20	21
22	23	24	25	26	27	28	27	28	29	30	31			24	25	26	27	28	29	30	22	23	24	25	26	27	28
29	30													24	25	26	27	28	29	30	29	30	31				

Impact on International Rail Freight

- Capacity reduction by 1/3
- Partially in the shadow of another major project in Italy
- Estimated extra running time: max 30 mins
- In annual timetable: yes

Impact of TCR 2025 at RFI (1)

Section Node of Genova + Genova - Ovada

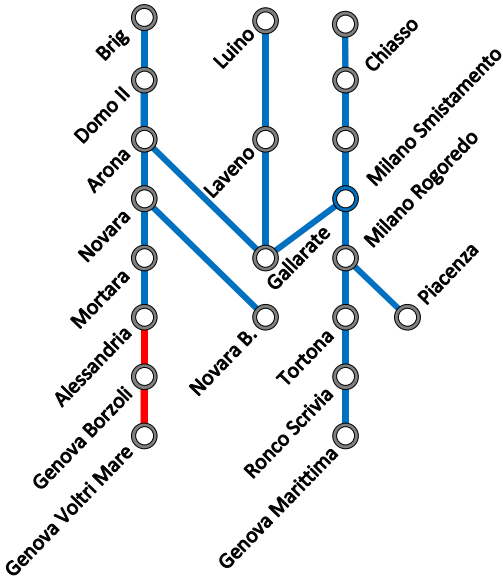

2025 Calendar

Single track operation Total closure

January							February							March							April						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	5						1	2						1	2		1	2	3	4	5	6
6	7	8	9	10	11	12	3	4	5	6	7	8	9	3	4	5	6	7	8	9	7	8	9	10	11	12	13
13	14	15	16	17	18	19	10	11	12	13	14	15	16	10	11	12	13	14	15	16	14	15	16	17	18	19	20
20	21	22	23	24	25	26	17	18	19	20	21	22	23	17	18	19	20	21	22	23	21	22	23	24	25	26	27
27	28	29	30	31			24	25	26	27	28			24	25	26	27	28	29	30	28	29	30				
														31													

May							June							July							August						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
			1	2	3	4							1												1	2	3
5	6	7	8	9	10	11	2	3	4	5	6	7	8	7	8	9	10	11	12	13	4	5	6	7	8	9	10
12	13	14	15	16	17	18	9	10	11	12	13	14	15	14	15	16	17	18	19	20	11	12	13	14	15	16	17
19	20	21	22	23	24	25	16	17	18	19	20	21	22	21	22	23	24	25	26	27	18	19	20	21	22	23	24
26	27	28	29	30	31		23	24	25	26	27	28	29	28	29	30	31				25	26	27	28	29	30	31
							30																				

September							October							November							December						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7			1	2	3	4	5						1	2		1	2	3	4	5	6
8	9	10	11	12	13	14	6	7	8	9	10	11	12	3	4	5	6	7	8	9	8	9	10	11	12	13	14
15	16	17	18	19	20	21	13	14	15	16	17	18	19	10	11	12	13	14	15	16	15	16	17	18	19	20	21
22	23	24	25	26	27	28	20	21	22	23	24	25	26	17	18	19	20	21	22	23	22	23	24	25	26	27	28
29							27	28	29	30	31			24	25	26	27	28	29	30	29	30	31				

Major Capacity Restriction

State of play : 22.08.2024

Disclaimer see front page


- Location:
Genova Sampierdarena Smistamento - Genova Marittima
Quadrivio Torbella (line Bastioni and Sussidiaria)
Genova Borzoli - Bivio Polcevera
Genova Borzoli - Genova Voltri (via PP Corvi)
Bivio Fegino (e) - Bivio Polcevera (i)
Alessandria - Ovada - Genova Borzoli
- Type: 30 days of Total Closure
- Period: 17.05.2025 - 15.06.2025
- Type of works:
III Valico project
Activities for Parco Fuorimuro
New Itinerary "Campasso"
Track renewal, line enhancement and civil works

Impact on International Rail Freight

- Cancellations: Yes. Cancelled trains with Origin/Destination Genova Voltri Fascio Merci and Genova Marittima.
- Deviations: Yes, via San Giuseppe di Cairo-Savona and via Genova Piazza Principe taking into consideration the residual capacity and with maximum length of 330meters.
- Estimated extra running time: related to the O/D of the trains
- In annual timetable: No

Impact of TCR 2025 at RFI (2)

Section Milano - Genova

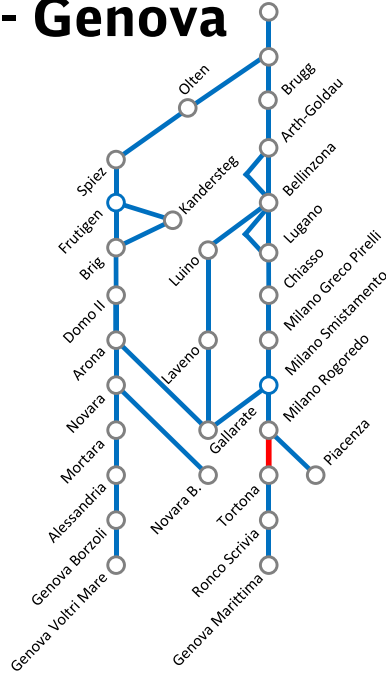

State of play : 22.08.2024
Disclaimer see front page

Major Capacity Restriction

- Location:
San Martino Cava Manara - Bressana Bottarone
- Type:
Phase 1) 50 days of track closure with periodical night line closure for 5h and 30minutes
Phase 2) 40 days of total closure
Phase 3) 30 days of track closure with periodical night line closure for 5h and 30minutes
- Period:
Phase 1) 01.06.2025 - 20.07.2025
Phase 2) 21.07.2025 - 29.08.2025
Phase 3) 30.08.2025 - 28.09.2025
- Type of works: Extraordinary maintenance of the bridge over the river Po

2025 Calendar

■ Single track operation ■ Total closure

January						
Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	5
6	7	8	9	10	11	12
13	14	15	16	17	18	19
20	21	22	23	24	25	26
27	28	29	30	31		

February						
Mo	Tu	We	Th	Fr	Sa	Su
					1	2
3	4	5	6	7	8	9
10	11	12	13	14	15	16
17	18	19	20	21	22	23
24	25	26	27	28		

March						
Mo	Tu	We	Th	Fr	Sa	Su
					1	2
3	4	5	6	7	8	9
10	11	12	13	14	15	16
17	18	19	20	21	22	23
24	25	26	27	28	29	30
31						

April						
Mo	Tu	We	Th	Fr	Sa	Su
	1	2	3	4	5	6
7	8	9	10	11	12	13
14	15	16	17	18	19	20
21	22	23	24	25	26	27
28	29	30				

May						
Mo	Tu	We	Th	Fr	Sa	Su
			1	2	3	4
5	6	7	8	9	10	11
12	13	14	15	16	17	18
19	20	21	22	23	24	25
26	27	28	29	30	31	

June						
Mo	Tu	We	Th	Fr	Sa	Su
						1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	29
30						

July						
Mo	Tu	We	Th	Fr	Sa	Su
	1	2	3	4	5	6
7	8	9	10	11	12	13
14	15	16	17	18	19	20
21	22	23	24	25	26	27
28	29	30	31			

August						
Mo	Tu	We	Th	Fr	Sa	Su
				1	2	3
4	5	6	7	8	9	10
11	12	13	14	15	16	17
18	19	20	21	22	23	24
25	26	27	28	29	30	31

September						
Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7
8	9	10	11	12	13	14
15	16	17	18	19	20	21
22	23	24	25	26	27	28
29	30					

October						
Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	5
6	7	8	9	10	11	12
13	14	15	16	17	18	19
20	21	22	23	24	25	26
27	28	29	30	31		

November						
Mo	Tu	We	Th	Fr	Sa	Su
					1	2
3	4	5	6	7	8	9
10	11	12	13	14	15	16
17	18	19	20	21	22	23
24	25	26	27	28	29	30


December						
Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7
8	9	10	11	12	13	14
15	16	17	18	19	20	21
22	23	24	25	26	27	28
29	30	31				

Impact on International Rail Freight

- Cancellations: Yes.
- Deviations: Yes, via Bologna-Prato, Mortara-Novara, Verona-Milano and Milano-Piacenza.
- Estimated extra running time: related to the O/D of the trains
- In annual timetable: No

Impact of TCR 2025 at RFI (3)

Section Milano - Domodossola + Arona - Oleggio

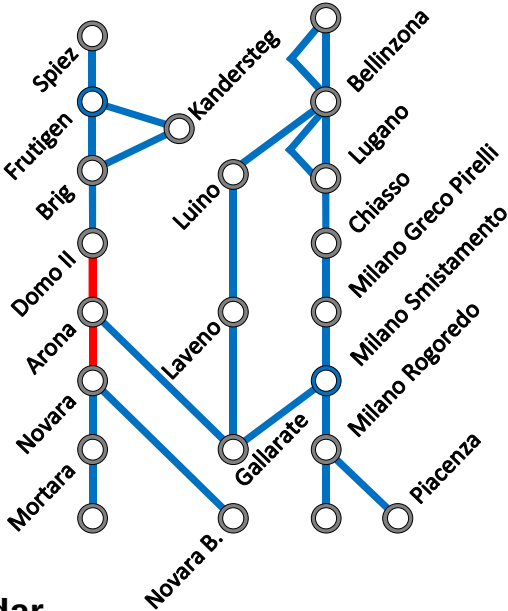

2025 Calendar
Single track operation Total closure

January						
Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	5
6	7	8	9	10	11	12
13	14	15	16	17	18	19
20	21	22	23	24	25	26
27	28	29	30	31		

February						
Mo	Tu	We	Th	Fr	Sa	Su
					1	2
3	4	5	6	7	8	9
10	11	12	13	14	15	16
17	18	19	20	21	22	23
24	25	26	27	28		

March						
Mo	Tu	We	Th	Fr	Sa	Su
					1	2
3	4	5	6	7	8	9
10	11	12	13	14	15	16
17	18	19	20	21	22	23
24	25	26	27	28	29	30
31						

April						
Mo	Tu	We	Th	Fr	Sa	Su
	1	2	3	4	5	6
7	8	9	10	11	12	13
14	15	16	17	18	19	20
21	22	23	24	25	26	27
28	29	30				

May						
Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	
5	6	7	8	9	10	11
12	13	14	15	16	17	18
19	20	21	22	23	24	25
26	27	28	29	30	31	

June						
Mo	Tu	We	Th	Fr	Sa	Su
						1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	29
30						

July						
Mo	Tu	We	Th	Fr	Sa	Su
	1	2	3	4	5	6
7	8	9	10	11	12	13
14	15	16	17	18	19	20
21	22	23	24	25	26	27
28	29	30	31			

August						
Mo	Tu	We	Th	Fr	Sa	Su
				1	2	3
4	5	6	7	8	9	10
11	12	13	14	15	16	17
18	19	20	21	22	23	24
25	26	27	28	29	30	31

September						
Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7
8	9	10	11	12	13	14
15	16	17	18	19	20	21
22	23	24	25	26	27	28
29	30					

October						
Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	5
6	7	8	9	10	11	12
13	14	15	16	17	18	19
20	21	22	23	24	25	26
27	28	29	30	31		

November						
Mo	Tu	We	Th	Fr	Sa	Su
					1	2
3	4	5	6	7	8	9
10	11	12	13	14	15	16
17	18	19	20	21	22	23
24	25	26	27	28	29	30

December						
Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7
8	9	10	11	12	13	14
15	16	17	18	19	20	21
22	23	24	25	26	27	28
29	30	31				

Major Capacity Restriction

State of play : 22.08.2024
Disclaimer see front page

- Location: Arona - Premosello Chiovenda
 - Type: 65 days of total closure divided in two period
 - Period: 08.06.2025 - 27.07.2025 and 30.08.2025-13.09.2025
 - Type of works: Gauge enhancement - P/C 80 + ERTMS + track renewal
- Location: Arona - Sesto Calende
 - Type: 50 days of track closure (in shadow to the previous TCR)
 - Period: 08.06.2025 - 27.07.2025
 - Type of works: Extraordinary maintenance to Sesto Calende bridge: km 43+316
- Location: Arona - Oleggio
 - Type: 30 days of total closure (in shadow to the first TCR)
 - Period: 28.06.2025 - 27.07.2025
 - Type of works: ERTMS

Impact on International Rail Freight


- Cancellations: Yes
- Deviations: Yes. Re-routing via Premosello - Borgomanero, or via Luino / Chiasso.
- Estimated extra running time: related to the O/D of the trains
- In annual timetable: Yes

Impact of TCR 2025 at RFI (4)

Section Node of Milan



State of play : 22.08.2024
Disclaimer see front page

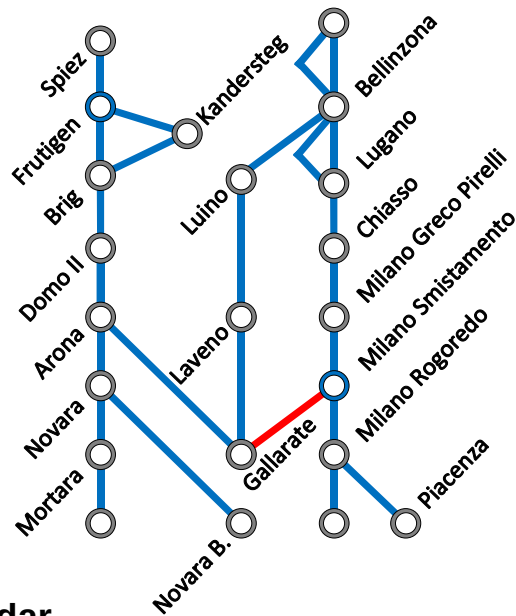

Major Capacity Restriction

- Location: Milano Certosa - Rho
- Type: 90 days of track closure of Varese line
- Period: 14.06.2025 - 14.09.2025
- Type of works: New station - Mind

2025 Calendar

Single track operation Total closure

January							February							March							April						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
			1	2	3	4	1					1	2						1	2							
6	7	8	9	10	11	12	3	4	5	6	7	8	9	3	4	5	6	7	8	9	7	8	9	10	11	12	13
13	14	15	16	17	18	19	10	11	12	13	14	15	16	10	11	12	13	14	15	16	14	15	16	17	18	19	20
20	21	22	23	24	25	26	17	18	19	20	21	22	23	17	18	19	20	21	22	23	21	22	23	24	25	26	27
27	28	29	30	31			24	25	26	27	28			24	25	26	27	28	29	30	28	29	30				
														31													

May							June							July							August						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
				1	2	3	2						1														
5	6	7	8	9	10	11	3	4	5	6	7	8	9	7	8	9	10	11	12	13	4	5	6	7	8	9	10
12	13	14	15	16	17	18	9	10	11	12	13	14	15	14	15	16	17	18	19	20	11	12	13	14	15	16	17
19	20	21	22	23	24	25	16	17	18	19	20	21	22	21	22	23	24	25	26	27	18	19	20	21	22	23	24
26	27	28	29	30	31		23	24	25	26	27	28	29	28	29	30	31				25	26	27	28	29	30	31
							30																				

September							October							November							December						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7				1	2	3	4								1	2	3	4	5	6	7
8	9	10	11	12	13	14	6	7	8	9	10	11	12	3	4	5	6	7	8	9	8	9	10	11	12	13	14
15	16	17	18	19	20	21	13	14	15	16	17	18	19	10	11	12	13	14	15	16	15	16	17	18	19	20	21
22	23	24	25	26	27	28	20	21	22	23	24	25	26	17	18	19	20	21	22	23	22	23	24	25	26	27	28
29	30						27	28	29	30	31			24	25	26	7	28	29	30	29	30	31				

Impact on International Rail Freight


- Cancellations: No
- Deviations: No deviations at the crossing points. There will be deviations on internal lines in R.F.I. network (via Alessandria - Piacenza)
- Estimated extra running time: related to the O/D of the trains
- In annual timetable: No

Impact of TCR 2025 at RFI (5)

Section Chiasso - Milano: station of Seregno



State of play : 22.08.2024
Disclaimer see front page

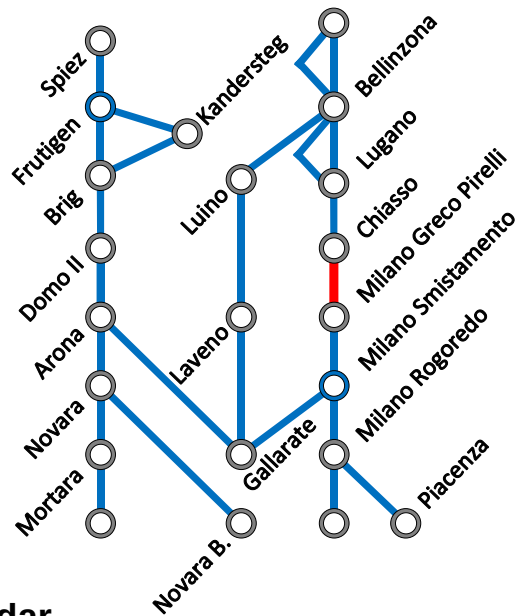

Major Capacity Restriction

- Location: Seregno
- Type: Track station closure - track VI and VII
- Period: 01.09.2025 - 13.12.2025 - exact period will be defined
- Type of works: Station upgrade

2025 Calendar

Single track operation Total closure

January						
Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	5
6	7	8	9	10	11	12
13	14	15	16	17	18	19
20	21	22	23	24	25	26
27	28	29	30	31		

February						
Mo	Tu	We	Th	Fr	Sa	Su
					1	2
3	4	5	6	7	8	9
10	11	12	13	14	15	16
17	18	19	20	21	22	23
24	25	26	27	28		

March						
Mo	Tu	We	Th	Fr	Sa	Su
					1	2
3	4	5	6	7	8	9
10	11	12	13	14	15	16
17	18	19	20	21	22	23
24	25	26	27	28	29	30
31						

April						
Mo	Tu	We	Th	Fr	Sa	Su
	1	2	3	4	5	6
7	8	9	10	11	12	13
14	15	16	17	18	19	20
21	22	23	24	25	26	27
28	29	30				

May						
Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	
5	6	7	8	9	10	11
12	13	14	15	16	17	18
19	20	21	22	23	24	25
26	27	28	29	30	31	

June						
Mo	Tu	We	Th	Fr	Sa	Su
					1	
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	29
30						

July						
Mo	Tu	We	Th	Fr	Sa	Su
	1	2	3	4	5	6
7	8	9	10	11	12	13
14	15	16	17	18	19	20
21	22	23	24	25	26	27
28	29	30	31			

August						
Mo	Tu	We	Th	Fr	Sa	Su
				1	2	3
4	5	6	7	8	9	10
11	12	13	14	15	16	17
18	19	20	21	22	23	24
25	26	27	28	29	30	31

September						
Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7
8	9	10	11	12	13	14
15	16	17	18	19	20	21
22	23	24	25	26	27	28
29	30					

October						
Mo	Tu	We	Th	Fr	Sa	Su
	1	2	3	4	5	
6	7	8	9	10	11	12
13	14	15	16	17	18	19
20	21	22	23	24	25	26
27	28	29	30	31		

November						
Mo	Tu	We	Th	Fr	Sa	Su
					1	2
3	4	5	6	7	8	9
10	11	12	13	14	15	16
17	18	19	20	21	22	23
24	25	26	27	28	29	30

December						
Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7
8	9	10	11	12	13	14
15	16	17	18	19	20	21
22	23	24	25	26	27	28
29	30	31				

Impact on International Rail Freight


- Cancellations: Yes, only for the trains with O/D the Seregno freight yard.
- Deviations: No
- Estimated extra running time: -
- In annual timetable: No

Impact of TCR 2025 at RFI (6)

Section Milano - Brescia



State of play : 22.08.2024
Disclaimer see front page

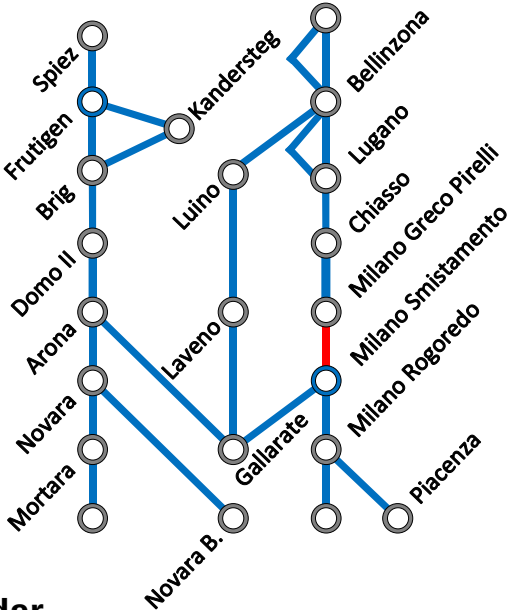

2025 Calendar

Single track operation Total closure

January							February							March							April						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
			1	2	3	4	3	4	5	6	7	8	9	3	4	5	6	7	8	9	7	8	9	10	11	12	13
6	7	8	9	10	11	12	10	11	12	13	14	15	16	10	11	12	13	14	15	16	14	15	16	17	18	19	20
13	14	15	16	17	18	19	17	18	19	20	21	22	23	17	18	19	20	21	22	23	21	22	23	24	25	26	27
20	21	22	23	24	25	26	24	25	26	27	28			24	25	26	27	28	29	30	28	29	30				
27	28	29	30	31										31													

May							June							July							August						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
				1	2	3	2	3	4	5	6	7	8	1	2	3	4	5	6	7	4	5	6	7	8	9	10
5	6	7	8	9	10	11	9	10	11	12	13	14	15	7	8	9	10	11	12	13	11	12	13	14	15	16	17
12	13	14	15	16	17	18	16	17	18	19	20	21	22	14	15	16	17	18	19	20	18	19	20	21	22	23	24
19	20	21	22	23	24	25	23	24	25	26	27	28	29	21	22	23	24	25	26	27	25	26	27	28	29	30	31
26	27	28	29	30	31									28	29	30	31										

September							October							November							December						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7	6	7	8	9	10	11	12	3	4	5	6	7	8	9	1	2	3	4	5	6	7
8	9	10	11	12	13	14	13	14	15	16	17	18	19	10	11	12	13	14	15	16	8	9	10	11	12	13	14
15	16	17	18	19	20	21	20	21	22	23	24	25	26	17	18	19	20	21	22	23	15	16	17	18	19	20	21
22	23	24	25	26	27	28	27	28	29	30	31			24	25	26	27	28	29	30	22	23	24	25	26	27	28
29	30						27	28	29	30	31			24	25	26	27	28	29	30	29	30	31				

Major Capacity Restriction

- Location:
 - Phase 1) Milano Lambrate - Pioltello (linea Venezia LL)
 - Phase 2) Milano Lambrate - Pioltello (linea Merci)
 - Phase 3) Milano Lambrate - Pioltello (linea Venezia DD)
 - Phase 4) Milano Lambrate - Pioltello (linea Venezia LL)
- Type: Total closure of 7 days for each phases
- Period:
 - Phase 1) 28.07.2025 - 03.08.2025
 - Phase 2) 04.08.2025 - 10.08.2025
 - Phase 3) 11.08.2025 - 17.08.2025
 - Phase 4) 18.08.2025 - 24.08.2025

Impact on International Rail Freight


- Cancellations: No
- Deviations: No deviations at the crossing points. There will be deviations on internal lines in R.F.I. network.
- Estimated extra running time: related to the O/D of the trains
- In annual timetable: No

Impact of TCR 2026 at ProRail

Section Kijfhoek – Zevenaar (A15 tracé)



State of play : 27.12.2023
Disclaimer see front page

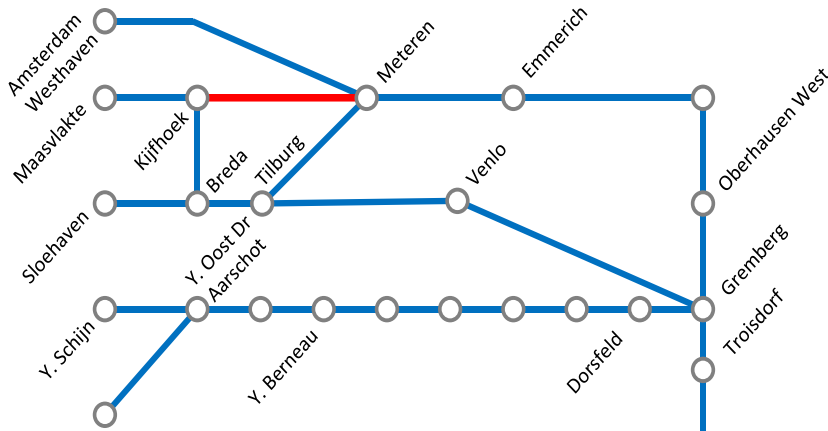

Major Capacity Restriction

- Location: Kijfhoek - Meteren - Zevenaar
- Type: Total Closure
- Period: Continuous
- Type of works: Type of works: Track & Rail, Tunnels, Catenary, Switch, Miscellaneous

2026 Calendar

Single track operation Total closure

January						
Mo	Tu	We	Th	Fr	Sa	Su
			1	2	3	4
5	6	7	8	9	10	11
12	13	14	15	16	17	18
19	20	21	22	23	24	25
26	27	28	29	30	31	

February						
Mo	Tu	We	Th	Fr	Sa	Su
						1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	

March						
Mo	Tu	We	Th	Fr	Sa	Su
						1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	29
30	31					

April						
Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	5
6	7	8	9	10	11	12
13	14	15	16	17	18	19
20	21	22	23	24	25	26
27	28	29	30			

May						
Mo	Tu	We	Th	Fr	Sa	Su
				1	2	3
4	5	6	7	8	9	10
11	12	13	14	15	16	17
18	19	20	21	22	23	24
25	26	27	28	29	30	31

June						
Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7
8	9	10	11	12	13	14
15	16	17	18	19	20	21
22	23	24	25	26	27	28
29	30					

July						
Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	5
6	7	8	9	10	11	12
13	14	15	16	17	18	19
20	21	22	23	24	25	26
27	28	29	30	31		

August						
Mo	Tu	We	Th	Fr	Sa	Su
					1	2
3	4	5	6	7	8	9
10	11	12	13	14	15	16
17	18	19	20	21	22	23
24	25	26	27	28	29	30
31						

September						
Mo	Tu	We	Th	Fr	Sa	Su
	1	2	3	4	5	6
7	8	9	10	11	12	13
14	15	16	17	18	19	20
21	22	23	24	25	26	27
28	29	30				

October						
Mo	Tu	We	Th	Fr	Sa	Su
			1	2	3	4
5	6	7	8	9	10	11
12	13	14	15	16	17	18
19	20	21	22	23	24	25
26	27	28	29	30	31	

November						
Mo	Tu	We	Th	Fr	Sa	Su
						1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	29
30						

December						
Mo	Tu	We	Th	Fr	Sa	Su
	1	2	3	4	5	6
7	8	9	10	11	12	13
14	15	16	17	18	19	20
21	22	23	24	25	26	27
28	29	30	31			

Impact on International Rail Freight


- Deviations: via Venlo and partly Bad Bentheim (RFC 8)
- Estimated extra running time: 30-60 minutes
- Restrictions for ad-hoc requests: limited capacity at Bad Bentheim and at Venlo
- Restrictions in train parameters: no
- Restrictions in container profile: no
- In annual timetable: no, timetables adapted 4 weeks before operation

Impact of TCR 2026 at ProRail

Section Amsterdam Westhaven – Meteren – Tilburg



State of play : 27.12.2023
Disclaimer see front page

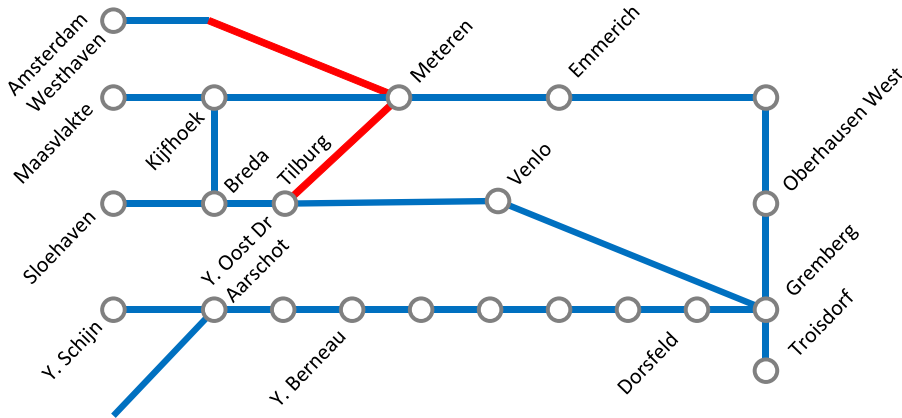

Major Capacity Restriction

- Location: Utrecht – Den Bosch (‘s-Hertogenbosch)
- Type: Total Closure
- Period: Continuous
- Type of works: Type of works: Track & Rail, Renewal, Bridge, Catenary, Switch, Miscellaneous

2026 Calendar

Single track operation Total closure

January						
Mo	Tu	We	Th	Fr	Sa	Su
			1	2	3	4
5	6	7	8	9	10	11
12	13	14	15	16	17	18
19	20	21	22	23	24	25
26	27	28	29	30	31	

February						
Mo	Tu	We	Th	Fr	Sa	Su
						1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	

March						
Mo	Tu	We	Th	Fr	Sa	Su
						1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	29
30	31					

April						
Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	5
6	7	8	9	10	11	12
13	14	15	16	17	18	19
20	21	22	23	24	25	26
27	28	29	30			

May						
Mo	Tu	We	Th	Fr	Sa	Su
				1	2	3
4	5	6	7	8	9	10
11	12	13	14	15	16	17
18	19	20	21	22	23	24
25	26	27	28	29	30	31

June						
Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7
8	9	10	11	12	13	14
15	16	17	18	19	20	21
22	23	24	25	26	27	28
29	30					

July						
Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	5
6	7	8	9	10	11	12
13	14	15	16	17	18	19
20	21	22	23	24	25	26
27	28	29	30	31		

August						
Mo	Tu	We	Th	Fr	Sa	Su
					1	2
3	4	5	6	7	8	9
10	11	12	13	14	15	16
17	18	19	20	21	22	23
24	25	26	27	28	29	30
31						

September						
Mo	Tu	We	Th	Fr	Sa	Su
	1	2	3	4	5	6
7	8	9	10	11	12	13
14	15	16	17	18	19	20
21	22	23	24	25	26	27
28	29	30				

October						
Mo	Tu	We	Th	Fr	Sa	Su
			1	2	3	4
5	6	7	8	9	10	11
12	13	14	15	16	17	18
19	20	21	22	23	24	25
26	27	28	29	30	31	

November						
Mo	Tu	We	Th	Fr	Sa	Su
						1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	29
30						

December						
Mo	Tu	We	Th	Fr	Sa	Su
	1	2	3	4	5	6
7	8	9	10	11	12	13
14	15	16	17	18	19	20
21	22	23	24	25	26	27
28	29	30	31			

Impact on International Rail Freight


- Deviations: Intern in the Netherlands, partly via Bad Bentheim (RFC 8)
- Estimated extra running time: 30-60 minutes
- Restrictions for ad-hoc requests: limited capacity at Bad Bentheim
- Restrictions in train parameters: no
- Restrictions in container profile: no
- In annual timetable: no

Impact of TCR 2026 at ProRail

Section Kijfhoek – Breda & Tilburg – Venlo



State of play : 27.12.2023
Disclaimer see front page

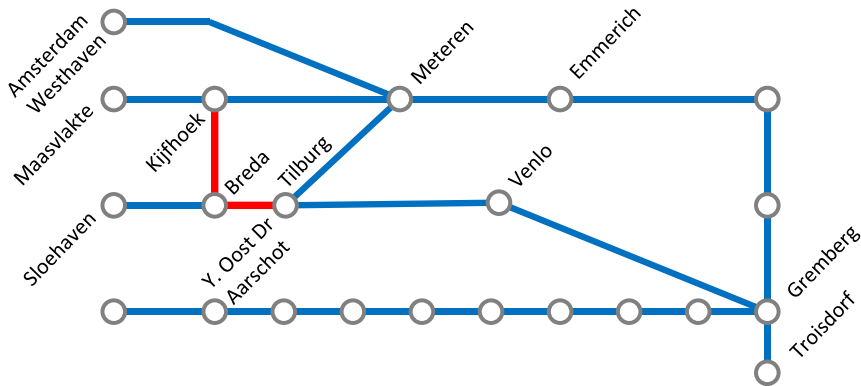

Major Capacity Restriction

- Location: Kijfhoek - Breda & Eindhoven
- Type: Total Closure, Single Track Operation
- Period: Continuous
- Type of works: Type of works: Track & Rail, Bridge, Catenary, Switch, Miscellaneous

2026 Calendar

Single track operation Total closure

January						
Mo	Tu	We	Th	Fr	Sa	Su
			1	2	3	4
5	6	7	8	9	10	11
12	13	14	15	16	17	18
19	20	21	22	23	24	25
26	27	28	29	30	31	

February						
Mo	Tu	We	Th	Fr	Sa	Su
						1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	

March						
Mo	Tu	We	Th	Fr	Sa	Su
						1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	29

April						
Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	5
6	7	8	9	10	11	12
13	14	15	16	17	18	19
20	21	22	23	24	25	26
27	28	29	30			

May						
Mo	Tu	We	Th	Fr	Sa	Su
				1	2	3
4	5	6	7	8	9	10
11	12	13	14	15	16	17
18	19	20	21	22	23	24
25	26	27	28	29	30	31

June						
Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7
8	9	10	11	12	13	14
15	16	17	18	19	20	21
22	23	24	25	26	27	28
29	30					

July						
Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	5
6	7	8	9	10	11	12
13	14	15	16	17	18	19
20	21	22	23	24	25	26
27	28	29	30	31		

August						
Mo	Tu	We	Th	Fr	Sa	Su
					1	2
3	4	5	6	7	8	9
10	11	12	13	14	15	16
17	18	19	20	21	22	23
24	25	26	27	28	29	30

September						
Mo	Tu	We	Th	Fr	Sa	Su
	1	2	3	4	5	6
7	8	9	10	11	12	13
14	15	16	17	18	19	20
21	22	23	24	25	26	27
28	29	30				

October						
Mo	Tu	We	Th	Fr	Sa	Su
			1	2	3	4
5	6	7	8	9	10	11
12	13	14	15	16	17	18
19	20	21	22	23	24	25
26	27	28	29	30	31	

November						
Mo	Tu	We	Th	Fr	Sa	Su
						1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	29

December						
Mo	Tu	We	Th	Fr	Sa	Su
	1	2	3	4	5	6
7	8	9	10	11	12	13
14	15	16	17	18	19	20
21	22	23	24	25	26	27
28	29	30	31			

Impact on International Rail Freight


- Deviations: via Betuweroute: 15-30 minutes
- Restrictions for ad-hoc requests: limited capacity at Betuweroute
- Restrictions in train parameters: no
- Restrictions in container profile: no
- In annual timetable: no

Impact of TCR 2026 at ProRail

Section Breda - Tilburg - Venlo



State of play : 27.12.2023
Disclaimer see front page

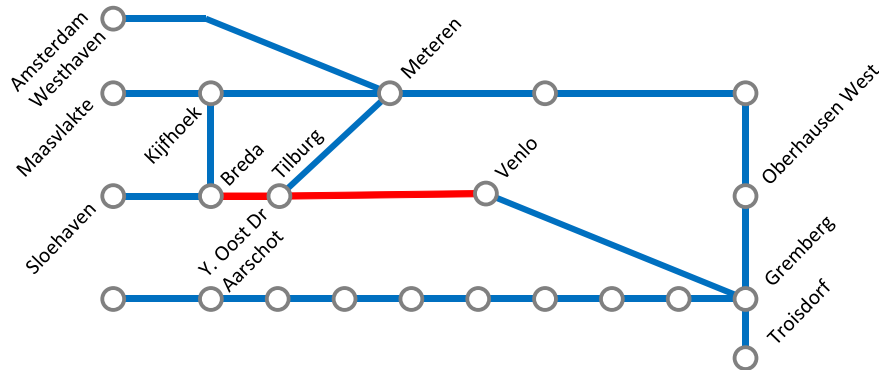

Major Capacity Restriction

- Location: Breda - Tilburg - Boxtel
- Type: Total Closure
- Period: Continuous
- Type of works: Type of works: Track & Rail, Catenary, Switch, Miscellaneous

2026 Calendar

Single track operation Total closure

January						
Mo	Tu	We	Th	Fr	Sa	Su
				1	2	3
4	5	6	7	8	9	10
11	12	13	14	15	16	17
18	19	20	21	22	23	24
25	26	27	28	29	30	31

February						
Mo	Tu	We	Th	Fr	Sa	Su
						1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	

March						
Mo	Tu	We	Th	Fr	Sa	Su
						1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	29
30	31					

April						
Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	5
6	7	8	9	10	11	12
13	14	15	16	17	18	19
20	21	22	23	24	25	26
27	28	29	30			

May						
Mo	Tu	We	Th	Fr	Sa	Su
				1	2	3
4	5	6	7	8	9	10
11	12	13	14	15	16	17
18	19	20	21	22	23	24
25	26	27	28	29	30	31

June						
Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7
8	9	10	11	12	13	14
15	16	17	18	19	20	21
22	23	24	25	26	27	28
29	30					

July						
Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	5
6	7	8	9	10	11	12
13	14	15	16	17	18	19
20	21	22	23	24	25	26
27	28	29	30	31		

August						
Mo	Tu	We	Th	Fr	Sa	Su
					1	2
3	4	5	6	7	8	9
10	11	12	13	14	15	16
17	18	19	20	21	22	23
24	25	26	27	28	29	30
31						

September						
Mo	Tu	We	Th	Fr	Sa	Su
	1	2	3	4	5	6
7	8	9	10	11	12	13
14	15	16	17	18	19	20
21	22	23	24	25	26	27
28	29	30				

October						
Mo	Tu	We	Th	Fr	Sa	Su
			1	2	3	4
5	6	7	8	9	10	11
12	13	14	15	16	17	18
19	20	21	22	23	24	25
26	27	28	29	30	31	

November						
Mo	Tu	We	Th	Fr	Sa	Su
						1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	29
30						

December						
Mo	Tu	We	Th	Fr	Sa	Su
	1	2	3	4	5	6
7	8	9	10	11	12	13
14	15	16	17	18	19	20
21	22	23	24	25	26	27
28	29	30	31			

Impact on International Rail Freight


- Deviations: via Betuweroute: 15-30 minutes
- Restrictions for ad-hoc requests: limited capacity at Betuweroute
- Restrictions in train parameters: no
- Restrictions in container profile: no
- In annual timetable: no

Impact of TCR 2026 at ProRail

Section Tilburg - Venlo



State of play : 27.12.2023
Disclaimer see front page

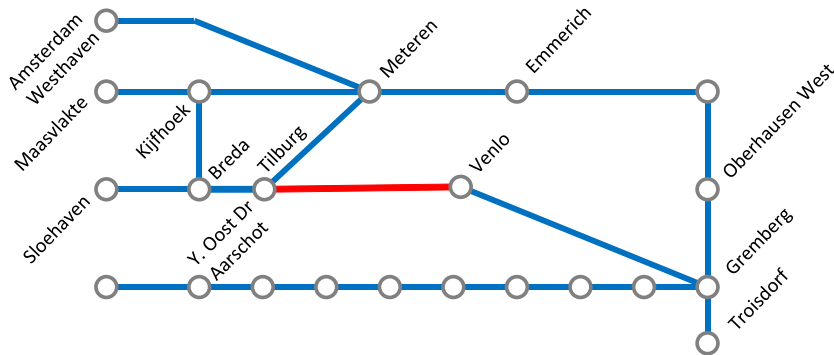

Major Capacity Restriction

- Location: Eindhoven - Venlo
- Type: Total Closure
- Period: Continuous
- Type of works: Type of works: Track & Rail, Catenary, Switch, Miscellaneous

2026 Calendar

■ Single track operation ■ Total closure

January						
Mo	Tu	We	Th	Fr	Sa	Su
			1	2	3	4
5	6	7	8	9	10	11
12	13	14	15	16	17	18
19	20	21	22	23	24	25
26	27	28	29	30	31	

February						
Mo	Tu	We	Th	Fr	Sa	Su
						1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	

March						
Mo	Tu	We	Th	Fr	Sa	Su
						1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	29
30	31					

April						
Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	5
6	7	8	9	10	11	12
13	14	15	16	17	18	19
20	21	22	23	24	25	26
27	28	29	30			

May						
Mo	Tu	We	Th	Fr	Sa	Su
				1	2	3
4	5	6	7	8	9	10
11	12	13	14	15	16	17
18	19	20	21	22	23	24
25	26	27	28	29	30	31

June						
Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7
8	9	10	11	12	13	14
15	16	17	18	19	20	21
22	23	24	25	26	27	28
29	30					

July						
Mo	Tu	We	Th	Fr	Sa	Su
						1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	29
30	31					

August						
Mo	Tu	We	Th	Fr	Sa	Su
						1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	29
30	31					

September						
Mo	Tu	We	Th	Fr	Sa	Su
	1	2	3	4	5	6
7	8	9	10	11	12	13
14	15	16	17	18	19	20
21	22	23	24	25	26	27
28	29	30				

October						
Mo	Tu	We	Th	Fr	Sa	Su
			1	2	3	4
5	6	7	8	9	10	11
12	13	14	15	16	17	18
19	20	21	22	23	24	25
26	27	28	29	30	31	

November						
Mo	Tu	We	Th	Fr	Sa	Su
						1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	29
30						

December						
Mo	Tu	We	Th	Fr	Sa	Su
	1	2	3	4	5	6
7	8	9	10	11	12	13
14	15	16	17	18	19	20
21	22	23	24	25	26	27
28	29	30	31			

Impact on International Rail Freight


- Deviations: via Betuweroute: 15-30 minutes
- Restrictions for ad-hoc requests: limited capacity at Betuweroute
- Restrictions in train parameters: no
- Restrictions in container profile: no
- In annual timetable: no

Impact of TCR 2026 at DB InfraGO AG

Section Emmerich Border - Oberhausen Main Station



State of play : 01.10.2024
Disclaimer see front page

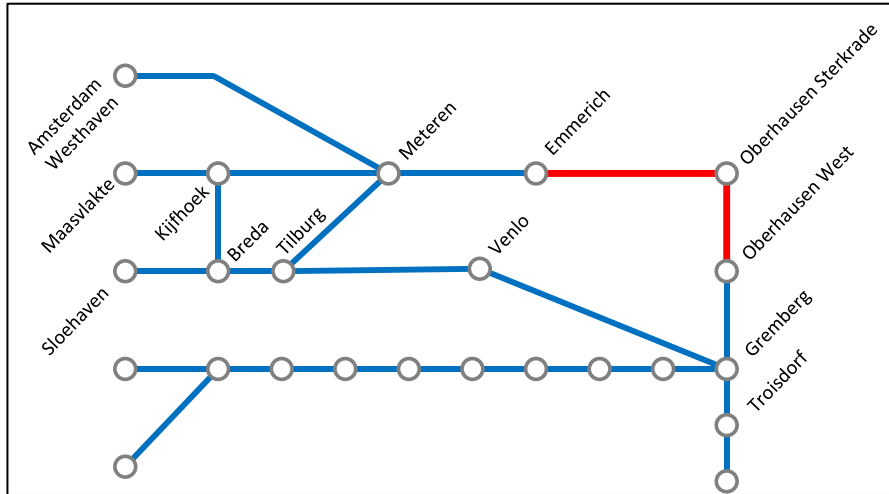

Major Capacity Restriction

- Location: Emmerich Border - Oberhausen Main Station
- Type: Total Closure, Single Track Operation
- Period: Continuous
- Type of works: Type of works: Track & Rail, Bridge, Catenary, Switch, Miscellaneous

2026 Calendar

 Single track operation Total closure

January						
Mo	Tu	We	Th	Fr	Sa	Su
			1	2	3	4
5	6	7	8	9	10	11
12	13	14	15	16	17	18
19	20	21	22	23	24	25
26	27	28	29	30	31	

February						
Mo	Tu	We	Th	Fr	Sa	Su
						1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	

March						
Mo	Tu	We	Th	Fr	Sa	Su
						1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	29
30	31					

April						
Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	5
6	7	8	9	10	11	12
13	14	15	16	17	18	19
20	21	22	23	24	25	26
27	28	29	30			

May						
Mo	Tu	We	Th	Fr	Sa	Su
				1	2	3
4	5	6	7	8	9	10
11	12	13	14	15	16	17
18	19	20	21	22	23	24
25	26	27	28	29	30	31

June						
Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7
8	9	10	11	12	13	14
15	16	17	18	19	20	21
22	23	24	25	26	27	28
29	30					

July						
Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	5
6	7	8	9	10	11	12
13	14	15	16	17	18	19
20	21	22	23	24	25	26
27	28	29	30	31		

August						
Mo	Tu	We	Th	Fr	Sa	Su
					1	2
3	4	5	6	7	8	9
10	11	12	13	14	15	16
17	18	19	20	21	22	23
24	25	26	27	28	29	30
31						

September						
Mo	Tu	We	Th	Fr	Sa	Su
	1	2	3	4	5	6
7	8	9	10	11	12	13
14	15	16	17	18	19	20
21	22	23	24	25	26	27
28	29	30				

October						
Mo	Tu	We	Th	Fr	Sa	Su
			1	2	3	4
5	6	7	8	9	10	11
12	13	14	15	16	17	18
19	20	21	22	23	24	25
26	27	28	29	30	31	

November						
Mo	Tu	We	Th	Fr	Sa	Su
						1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	29
30						

December						
Mo	Tu	We	Th	Fr	Sa	Su
	1	2	3	4	5	6
7	8	9	10	11	12	13
14	15	16	17	18	19	20
21	22	23	24	25	26	27
28	29	30	31			

Impact on International Rail Freight


- Cancellations: Yes
- Deviations: Yes
- Estimated extra running time: Detailed information on extra running time is distributed by DB InfraGO individually for every customer for each affected train. Additionally DB InfraGO offers train path advice free of charge
- In annual timetable: Yes

Impact of TCR 2026 at SBB Infra (1)

Section Arth-Goldau - Bellinzona (Gotthard base tunnel)



State of play : 12.12.2023
Disclaimer see front page

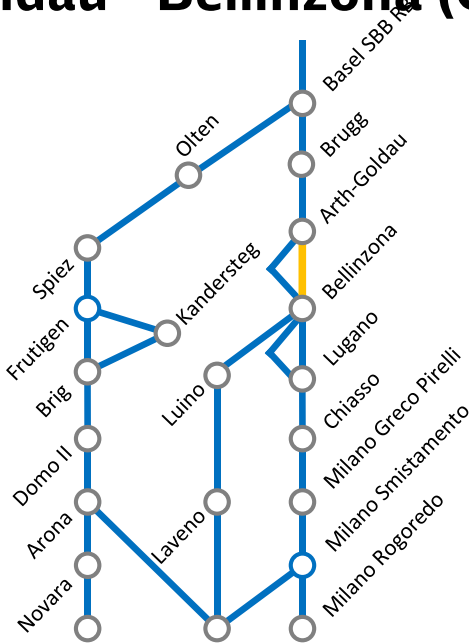

2026 Calendar

 Single track operation Total closure

January							February							March							April						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
5	6	7	8	9	10	11	2	3	4	5	6	7	8	2	3	4	5	6	7	8	6	7	8	9	10	11	12
12	13	14	15	16	17	18	9	10	11	12	13	14	15	9	10	11	12	13	14	15	13	14	15	16	17	18	19
19	20	21	22	23	24	25	16	17	18	19	20	21	22	16	17	18	19	20	21	22	20	21	22	23	24	25	26
26	27	28	29	30	31		23	24	25	26	27	28		23	24	25	26	27	28	29	27	28	29	30			
														30	31												

May							June							July							August						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
							1	2	3	4	5	6	7	1	2	3	4	5	6	7	1	2	3	4	5	6	7
4	5	6	7	8	9	10	8	9	10	11	12	13	14	6	7	8	9	10	11	12	3	4	5	6	7	8	9
11	12	13	14	15	16	17	15	16	17	18	19	20	21	13	14	15	16	17	18	19	10	11	12	13	14	15	16
18	19	20	21	22	23	24	22	23	24	25	26	27	28	20	21	22	23	24	25	26	17	18	19	20	21	22	23
25	26	27	28	29	30	31	29	30						27	28	29	30	31			24	25	26	27	28	29	30
																					31						

September							October							November							December						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
	1	2	3	4	5	6																					
7	8	9	10	11	12	13	5	6	7	8	9	10	11	2	3	4	5	6	7	8	7	8	9	10	11	12	13
14	15	16	17	18	19	20	12	13	14	15	16	17	18	9	10	11	12	13	14	15	14	15	16	17	18	19	20
21	22	23	24	25	26	27	19	20	21	22	23	24	25	16	17	18	19	20	21	22	21	22	23	24	25	26	27
28	29	30					26	27	28	29	30	31		23	24	25	26	27	28	29	28	29	30	31			
														30													

Major Capacity Restriction

- Location: Gotthard Base Tunnel
- Type: Single Track Operation
- Period: 31.12.2025 - 24.01.2026 (dates see below)
- Type of works: maintenance

Impact on International Rail Freight


- Capacity reduction from 1/3 to 3/4
- No deviations planned due to low volumes expected
- Estimated extra running time: 30 to 60 mins
- In annual timetable: no

Impact of TCR 2026 at SBB Infra (2)

Section Arth-Goldau - Bellinzona



State of play : 12.12.2023
Disclaimer see front page

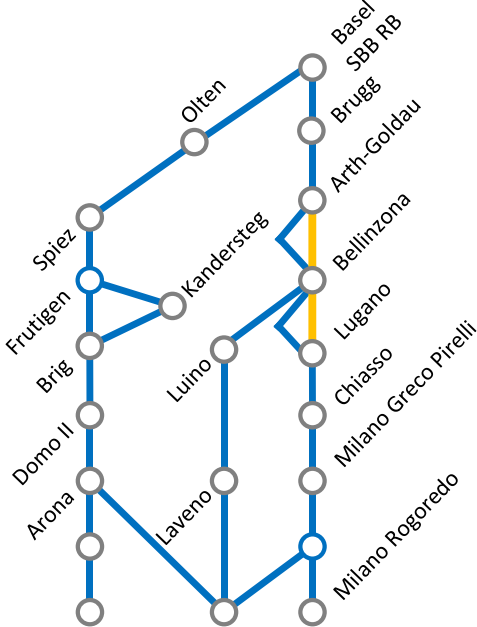

Major Capacity Restriction

- Location: Sisikon-Flüelen
- Type: Single Track Operation
- Period:14.12.2025-16.02.2026 / 26.07.2026-06.09.2026
- Type of works: Axenberg/Stutzeck tunnel renovation

2026 Calendar

Single track operation Total closure

January							February							March							April						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
				1	2	3	1						1														
5	6	7	8	9	10	11	2	3	4	5	6	7	8	2	3	4	5	6	7	8	6	7	8	9	10	11	12
12	13	14	15	16	17	18	9	10	11	12	13	14	15	9	10	11	12	13	14	15	13	14	15	16	17	18	19
19	20	21	22	23	24	25	16	17	18	19	20	21	22	16	17	18	19	20	21	22	20	21	22	23	24	25	26
26	27	28	29	30	31		23	24	25	26	27	28		23	24	25	26	27	28	29	27	28	29	30			
														30	31												

May							June							July							August						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
					1	2	1	2	3	4	5	6	7				1	2	3	4						1	2
4	5	6	7	8	9	10	8	9	10	11	12	13	14	6	7	8	9	10	11	12	3	4	5	6	7	8	9
11	12	13	14	15	16	17	15	16	17	18	19	20	21	13	14	15	16	17	18	19	10	11	12	13	14	15	16
18	19	20	21	22	23	24	22	23	24	25	26	27	28	20	21	22	23	24	25	26	17	18	19	20	21	22	23
25	26	27	28	29	30	31	29	30						27	28	29	30	31			24	25	26	27	28	29	30
																					31						

September							October							November							December						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
					1	2																					
7	8	9	10	11	12	13	5	6	7	8	9	10	11	2	3	4	5	6	7	8	7	8	9	10	11	12	13
14	15	16	17	18	19	20	12	13	14	15	16	17	18	9	10	11	12	13	14	15	14	15	16	17	18	19	20
21	22	23	24	25	26	27	19	20	21	22	23	24	25	16	17	18	19	20	21	22	21	22	23	24	25	26	27
28	29	30					26	27	28	29	30	31		23	24	25	26	27	28	29	28	29	30	31			
														30													

Impact on International Rail Freight


- Capacity reduction by circa 50% (excluding at night)
- Deviations via Simplon line
- Estimated extra running time: 30 mins
- In annual timetable: no

Impact of TCR 2026 at SBB Infra (3)

Section Arth-Goldau - Bellinzona



State of play : 12.12.2023
Disclaimer see front page

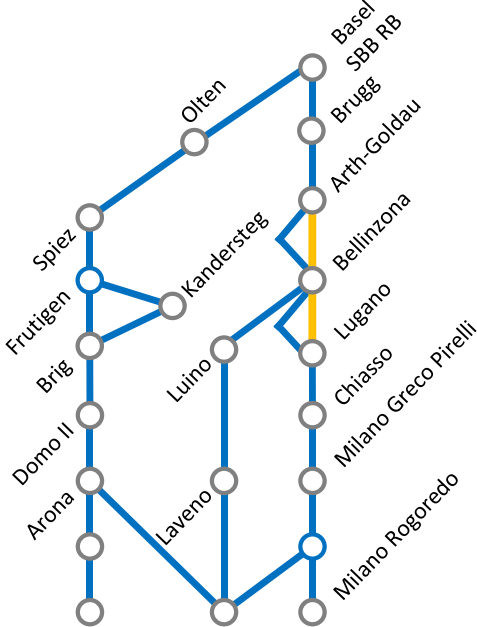

Major Capacity Restriction

- Location: Bellinzona-Castione-Arbedo
- Type: Single Track Operation
- Period: 20.06.2026 – 27.07.2026
- Type of works: new maintenance shop and station

2026 Calendar

 Single track operation Total closure

January							February							March							April						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
													1							1							
5	6	7	8	9	10	11	2	3	4	5	6	7	8	2	3	4	5	6	7	8	6	7	8	9	10	11	12
12	13	14	15	16	17	18	9	10	11	12	13	14	15	9	10	11	12	13	14	15	13	14	15	16	17	18	19
19	20	21	22	23	24	25	16	17	18	19	20	21	22	16	17	18	19	20	21	22	20	21	22	23	24	25	26
26	27	28	29	30	31		23	24	25	26	27	28	29	23	24	25	26	27	28	29	27	28	29	30			
														30	31												

May							June							July							August						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
							1	2	3	4	5	6	7														
4	5	6	7	8	9	10	8	9	10	11	12	13	14	6	7	8	9	10	11	12	3	4	5	6	7	8	9
11	12	13	14	15	16	17	15	16	17	18	19	20	21	13	14	15	16	17	18	19	10	11	12	13	14	15	16
18	19	20	21	22	23	24	22	23	24	25	26	27	28	20	21	22	23	24	25	26	17	18	19	20	21	22	23
25	26	27	28	29	30	31	29	30						27	28	29	30	31			24	25	26	27	28	29	30
																					31						

September							October							November							December						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
	1	2	3	4	5	6	5	6	7	8	9	10	11	2	3	4	5	6	7	8	7	8	9	10	11	12	13
7	8	9	10	11	12	13	12	13	14	15	16	17	18	9	10	11	12	13	14	15	14	15	16	17	18	19	20
14	15	16	17	18	19	20	19	20	21	22	23	24	25	16	17	18	19	20	21	22	21	22	23	24	25	26	27
21	22	23	24	25	26	27	26	27	28	29	30	31		23	24	25	26	27	28	29	28	29	30	31			
28	29	30												30													

Impact on International Rail Freight


- Capacity reduction by 50% (in the shadow of #2)
- Deviations via Simplon line
- Estimated extra running time: max 30 mins
- In annual timetable: tbd

Impact of TCR 2026 at SBB Infra (4)

Section Basel RB - Spiez



State of play : 12.12.2023
Disclaimer see front page

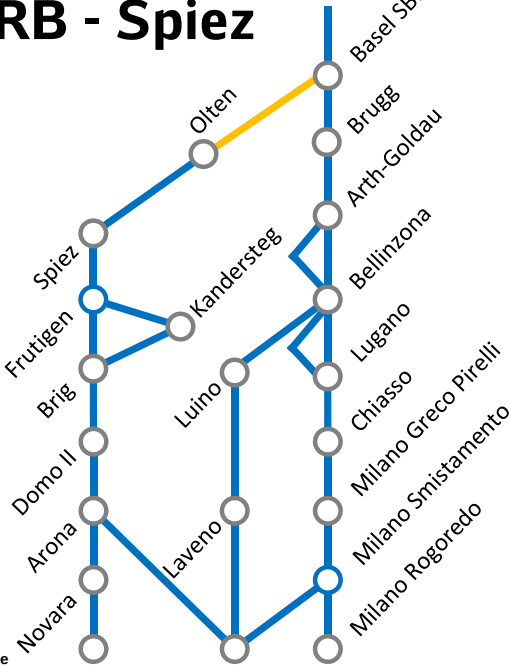

2026 Calendar

Single track operation Total closure

January						
Mo	Tu	We	Th	Fr	Sa	Su
			1	2	3	4
5	6	7	8	9	10	11
12	13	14	15	16	17	18
19	20	21	22	23	24	25
26	27	28	29	30	31	

February						
Mo	Tu	We	Th	Fr	Sa	Su
						1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	

March						
Mo	Tu	We	Th	Fr	Sa	Su
						1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	29
30	31					

April						
Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	5
6	7	8	9	10	11	12
13	14	15	16	17	18	19
20	21	22	23	24	25	26
27	28	29	30			

May						
Mo	Tu	We	Th	Fr	Sa	Su
				1	2	3
4	5	6	7	8	9	10
11	12	13	14	15	16	17
18	19	20	21	22	23	24
25	26	27	28	29	30	31

June						
Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7
8	9	10	11	12	13	14
15	16	17	18	19	20	21
22	23	24	25	26	27	28
29	30					

July						
Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	5
6	7	8	9	10	11	12
13	14	15	16	17	18	19
20	21	22	23	24	25	26
27	28	29	30	31		

August						
Mo	Tu	We	Th	Fr	Sa	Su
					1	2
3	4	5	6	7	8	9
10	11	12	13	14	15	16
17	18	19	20	21	22	23
24	25	26	27	28	29	30
31						

September						
Mo	Tu	We	Th	Fr	Sa	Su
	1	2	3	4	5	6
7	8	9	10	11	12	13
14	15	16	17	18	19	20
21	22	23	24	25	26	27
28	29	30				

October						
Mo	Tu	We	Th	Fr	Sa	Su
			1	2	3	4
5	6	7	8	9	10	11
12	13	14	15	16	17	18
19	20	21	22	23	24	25
26	27	28	29	30	31	

November						
Mo	Tu	We	Th	Fr	Sa	Su
						1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	29
30						

December						
Mo	Tu	We	Th	Fr	Sa	Su
	1	2	3	4	5	6
7	8	9	10	11	12	13
14	15	16	17	18	19	20
21	22	23	24	25	26	27
28	29	30	31			

Major Capacity Restriction

- Location: Hauenstein base tunnel
- Type: Single Track Operation (3/6 sections)
- Period: 31.05.2026 – 27.07.2026
- Type of works: track renewal

Impact on International Rail Freight


- Capacity reduction by $\frac{3}{4}$
- In the **shadow of major projects** in Germany and Italy
- Estimated extra running time: max 30 mins
- In annual timetable: no

Impact of TCR 2026 at SBB Infra (5)

Section Spiez-Domodossola



State of play : 01.10.2024
Disclaimer see front page

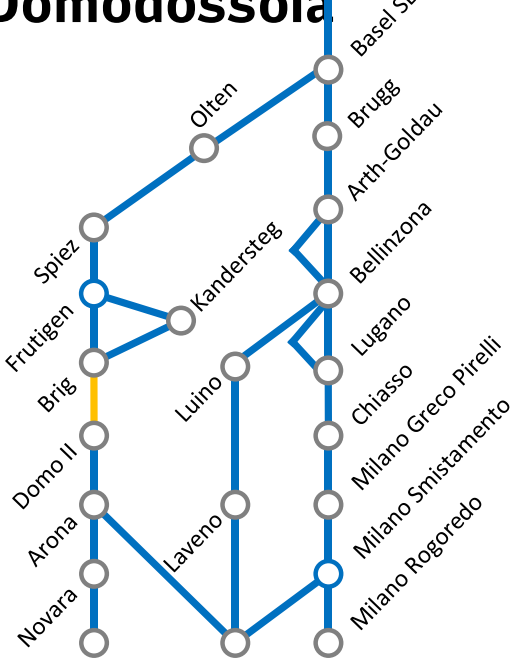

2026 Calendar

Single track operation Total closure

January						
Mo	Tu	We	Th	Fr	Sa	Su
			1	2	3	4
5	6	7	8	9	10	11
12	13	14	15	16	17	18
19	20	21	22	23	24	25
26	27	28	29	30	31	

February						
Mo	Tu	We	Th	Fr	Sa	Su
						1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	

March						
Mo	Tu	We	Th	Fr	Sa	Su
						1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	29
30	31					

April						
Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	5
6	7	8	9	10	11	12
13	14	15	16	17	18	19
20	21	22	23	24	25	26
27	28	29	30			

May						
Mo	Tu	We	Th	Fr	Sa	Su
				1	2	3
4	5	6	7	8	9	10
11	12	13	14	15	16	17
18	19	20	21	22	23	24
25	26	27	28	29	30	31

June						
Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7
8	9	10	11	12	13	14
15	16	17	18	19	20	21
22	23	24	25	26	27	28
29	30					

July						
Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	5
6	7	8	9	10	11	12
13	14	15	16	17	18	19
20	21	22	23	24	25	26
27	28	29	30	31		

August						
Mo	Tu	We	Th	Fr	Sa	Su
					1	2
3	4	5	6	7	8	9
10	11	12	13	14	15	16
17	18	19	20	21	22	23
24	25	26	27	28	29	30
31						

September						
Mo	Tu	We	Th	Fr	Sa	Su
	1	2	3	4	5	6
7	8	9	10	11	12	13
14	15	16	17	18	19	20
21	22	23	24	25	26	27
28	29	30				

October						
Mo	Tu	We	Th	Fr	Sa	Su
			1	2	3	4
5	6	7	8	9	10	11
12	13	14	15	16	17	18
19	20	21	22	23	24	25
26	27	28	29	30	31	

November						
Mo	Tu	We	Th	Fr	Sa	Su
						1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	29
30						

December						
Mo	Tu	We	Th	Fr	Sa	Su
	1	2	3	4	5	6
7	8	9	10	11	12	13
14	15	16	17	18	19	20
21	22	23	24	25	26	27
28	29	30	31			

Major Capacity Restriction


- Location: Simplon tunnel
- Type: Single Track Operation (1/4 sections)
- Period:16.02.2026 – 26.07.2026
- Type of works: track and tunnel vault renovation

Impact on International Rail Freight

- Capacity reduction by 1/3
- Partially in the shadow of another major project in Italy
- Estimated extra running time: max 30 mins
- In annual timetable: yes

Impact of TCR 2026 at RFI (1)

Section Novi Ligure - Arquata Scrivia

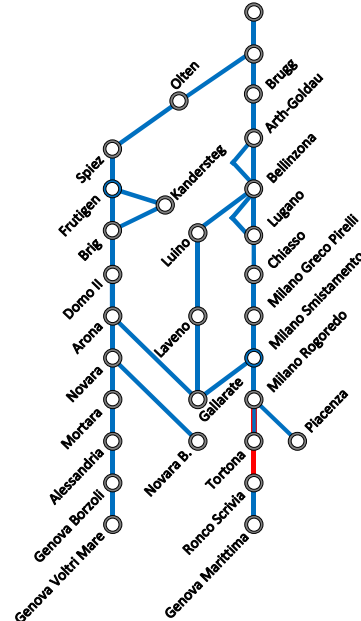

Major Capacity Restriction

- Location: Novi Ligure - Arquata Scrivia
- Type: 30 days of total closure
- Period: 01.01.2026 - 31.01.2026
- Type of works: III Valico Project

2026 Calendar

 Single track operation Total closure

January							February							March							April						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
				1	2	3	4						1							1							
5	6	7	8	9	10	11	2	3	4	5	6	7	8	2	3	4	5	6	7	8	6	7	8	9	10	11	12
12	13	14	15	16	17	18	9	10	11	12	13	14	15	9	10	11	12	13	14	15	13	14	15	16	17	18	19
19	20	21	22	23	24	25	16	17	18	19	20	21	22	16	17	18	19	20	21	22	20	21	22	23	24	25	26
26	27	28	29	30	31		23	24	25	26	27	28		23	24	25	26	27	28	29	27	28	29	30			
														30	31												

May							June							July							August						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
				1	2	3	1	2	3	4	5	6	7	6	7	8	9	10	11	12	3	4	5	6	7	8	9
4	5	6	7	8	9	10	8	9	10	11	12	13	14	6	7	8	9	10	11	12	10	11	12	13	14	15	16
11	12	13	14	15	16	17	15	16	17	18	19	20	21	13	14	15	16	17	18	19	17	18	19	20	21	22	23
18	19	20	21	22	23	24	22	23	24	25	26	27	28	20	21	22	23	24	25	26	24	25	26	27	28	29	30
25	26	27	28	29	30	31	29	30						27	28	29	30	31			31						


September							October							November							December						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
	1	2	3	4	5	6							1							1							
7	8	9	10	11	12	13	5	6	7	8	9	10	11	2	3	4	5	6	7	8	7	8	9	10	11	12	13
14	15	16	17	18	19	20	12	13	14	15	16	17	18	9	10	11	12	13	14	15	14	15	16	17	18	19	20
21	22	23	24	25	26	27	19	20	21	22	23	24	25	16	17	18	19	20	21	22	21	22	23	24	25	26	27
28	29	30					26	27	28	29	30	31		23	24	25	26	7	28	29	28	29	30	31			

Impact on International Rail Freight

- Cancellations: Yes
- Deviations: Yes, rerouting via Tortona - Arquata Scrivia or via Piacenza - Prato /Pontremoli or via San Giuseppe di Cairo or via Ovada in the residual capacity of the line.
- Estimated extra running time: related to the O/D of the trains
- In annual timetable: No

Impact of TCR 2026 at RFI (2)

Section Node of Genova

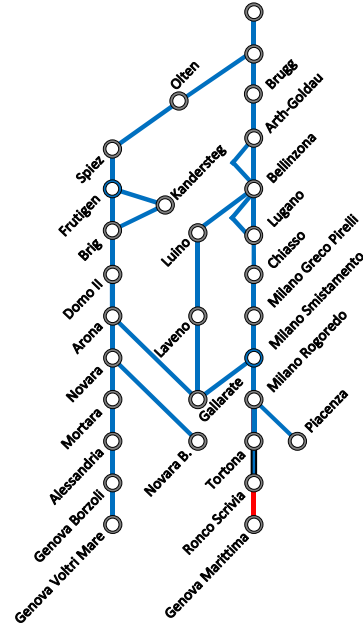

2026 Calendar

Single track operation Total closure

January							February							March							April						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
				1	2	3	4						1							1							
5	6	7	8	9	10	11	2	3	4	5	6	7	8	2	3	4	5	6	7	8	6	7	8	9	10	11	12
12	13	14	15	16	17	18	9	10	11	12	13	14	15	9	10	11	12	13	14	15	13	14	15	16	17	18	19
19	20	21	22	23	24	25	16	17	18	19	20	21	22	16	17	18	19	20	21	22	20	21	22	23	24	25	26
26	27	28	29	30	31		23	24	25	26	27	28		23	24	25	26	27	28	29	27	28	29	30			
														30	31												

May							June							July							August						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
				1	2	3	1	2	3	4	5	6	7	6	7	8	9	10	11	12	3	4	5	6	7	8	9
4	5	6	7	8	9	10	8	9	10	11	12	13	14	6	7	8	9	10	11	12	10	11	12	13	14	15	16
11	12	13	14	15	16	17	15	16	17	18	19	20	21	13	14	15	16	17	18	19	17	18	19	20	21	22	23
18	19	20	21	22	23	24	22	23	24	25	26	27	28	20	21	22	23	24	25	26	24	25	26	27	28	29	30
25	26	27	28	29	30	31	29	30						27	28	29	30	31			31						

September							October							November							December						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
	1	2	3	4	5	6							1	2	3	4	5	6	7	8	1	2	3	4	5	6	
7	8	9	10	11	12	13	5	6	7	8	9	10	11	2	3	4	5	6	7	8	7	8	9	10	11	12	13
14	15	16	17	18	19	20	12	13	14	15	16	17	18	9	10	11	12	13	14	15	14	15	16	17	18	19	20
21	22	23	24	25	26	27	19	20	21	22	23	24	25	16	17	18	19	20	21	22	21	22	23	24	25	26	27
28	29	30					26	27	28	29	30	31		23	24	25	26	7	28	29	28	29	30	31			

Major Capacity Restriction

- Location:
Genova San Quirico - Bivio Fegino (via Mignanego)
- Type: 30 days of total closure
- Period: 01.08.2026 - 31.08.2026
- Type of works: track renewal - phase 1


Impact on International Rail Freight

- Cancellations: No
- Deviations: Yes, rerouting via Busalla or in other rerouting lines
- Estimated extra running time: related to the O/D of the trains
- In annual timetable: No

Impact of TCR 2026 at RFI (3)

Section Genova - Ovada

State of play : 22.08.2024
Disclaimer see front page

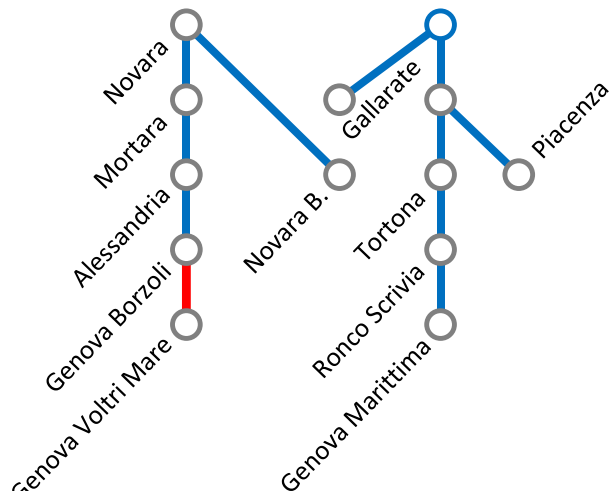

Major Capacity Restriction

- Location: Genova - Ovada
- Type: 30 days of total closure
- Period: 01.01.2026 - 30.06.2026 - exact period will be defined
- Type of works: Line enhancement + new underpass + switches renewal

2026 Calendar

Single track operation Total closure

January							February							March							April						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
				1	2	3							1										1	2	3	4	5
5	6	7	8	9	10	11	2	3	4	5	6	7	8	2	3	4	5	6	7	8	6	7	8	9	10	11	12
12	13	14	15	16	17	18	9	10	11	12	13	14	15	9	10	11	12	13	14	15	13	14	15	16	17	18	19
19	20	21	22	23	24	25	16	17	18	19	20	21	22	16	17	18	19	20	21	22	20	21	22	23	24	25	26
26	27	28	29	30	31		23	24	25	26	27	28		23	24	25	26	27	28	29	27	28	29	30			
														30	31												

May							June							July							August						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
				1	2	3	1	2	3	4	5	6	7			1	2	3	4	5					1	2	
4	5	6	7	8	9	10	8	9	10	11	12	13	14	6	7	8	9	10	11	12	3	4	5	6	7	8	9
11	12	13	14	15	16	17	15	16	17	18	19	20	21	13	14	15	16	17	18	19	10	11	12	13	14	15	16
18	19	20	21	22	23	24	22	23	24	25	26	27	28	20	21	22	23	24	25	26	17	18	19	20	21	22	23
25	26	27	28	29	30	31	29	30						27	28	29	30	31			24	25	26	27	28	29	30
																					31						

September							October							November							December						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
	1	2	3	4	5	6					1	2	3							1							
7	8	9	10	11	12	13	5	6	7	8	9	10	11	2	3	4	5	6	7	8	7	8	9	10	11	12	13
14	15	16	17	18	19	20	12	13	14	15	16	17	18	9	10	11	12	13	14	15	14	15	16	17	18	19	20
21	22	23	24	25	26	27	19	20	21	22	23	24	25	16	17	18	19	20	21	22	21	22	23	24	25	26	27
28	29	30					26	27	28	29	30	31		23	24	25	26	27	28	29	28	29	30	31			
														30													


Impact on International Rail Freight

- Cancellations: No
- Deviations: Yes
- Estimated extra running time: related to the O/D of the trains
- In annual timetable: No

Impact of TCR 2026 at RFI (4)

Section Milano - Genova

State of play : 22.08.2024
Disclaimer see front page

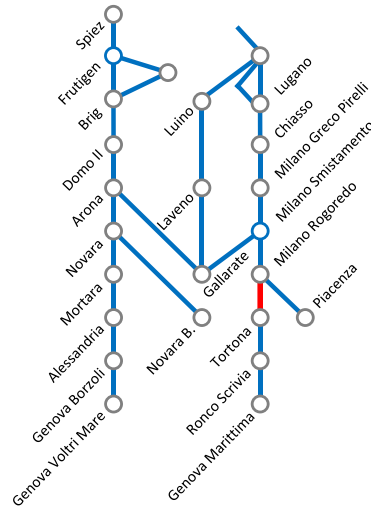

2026 Calendar

 Single track operation Total closure

January							February							March							April						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
5	6	7	8	9	10	11	2	3	4	5	6	7	8	2	3	4	5	6	7	8	6	7	8	9	10	11	12
12	13	14	15	16	17	18	9	10	11	12	13	14	15	9	10	11	12	13	14	15	13	14	15	16	17	18	19
19	20	21	22	23	24	25	16	17	18	19	20	21	22	16	17	18	19	20	21	22	20	21	22	23	24	25	26
26	27	28	29	30	31		23	24	25	26	27	28		23	24	25	26	27	28	29	27	28	29	30			
														30	31												

May							June							July							August						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
					1	2	1	2	3	4	5	6	7			1	2	3	4	5					1	2	
4	5	6	7	8	9	10	8	9	10	11	12	13	14	6	7	8	9	10	11	12	3	4	5	6	7	8	9
11	12	13	14	15	16	17	15	16	17	18	19	20	21	13	14	15	16	17	18	19	10	11	12	13	14	15	16
18	19	20	21	22	23	24	22	23	24	25	26	27	28	20	21	22	23	24	25	26	17	18	19	20	21	22	23
25	26	27	28	29	30	31	29	30						27	28	29	30	31			24	25	26	27	28	29	30
																					31						

September							October							November							December						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
	1	2	3	4	5	6														1							
7	8	9	10	11	12	13	5	6	7	8	9	10	11	2	3	4	5	6	7	8	7	8	9	10	11	12	13
14	15	16	17	18	19	20	12	13	14	15	16	17	18	9	10	11	12	13	14	15	14	15	16	17	18	19	20
21	22	23	24	25	26	27	19	20	21	22	23	24	25	16	17	18	19	20	21	22	21	22	23	24	25	26	27
28	29	30					26	27	28	29	30	31		23	24	25	26	27	28	29	28	29	30	31			
														30													

Major Capacity Restriction

- Location:
San Martino Cava Manara - Bressana Bottarone
- Type:
Phase 1) 40 days of total closure
Phase 2) 2x40 days of track closure
(40 days before the total closure and 40 days after)
- Period: 01.05.2026 - 30.09.2026 - exact period for each phases will be defined
- Type of works: Extraordinary maintenance of the bridge over the river Po


Impact on International Rail Freight

- Cancellations: Yes.
- Deviations: Yes, via Bologna-Prato, Mortara-Novara, Verona-Milano and Milano-Piacenza.
- Estimated extra running time: related to the O/D of the trains
- In annual timetable: No

Impact of TCR 2026 at RFI (5)

Section Node of Milan

State of play : 22.08.2024
Disclaimer see front page

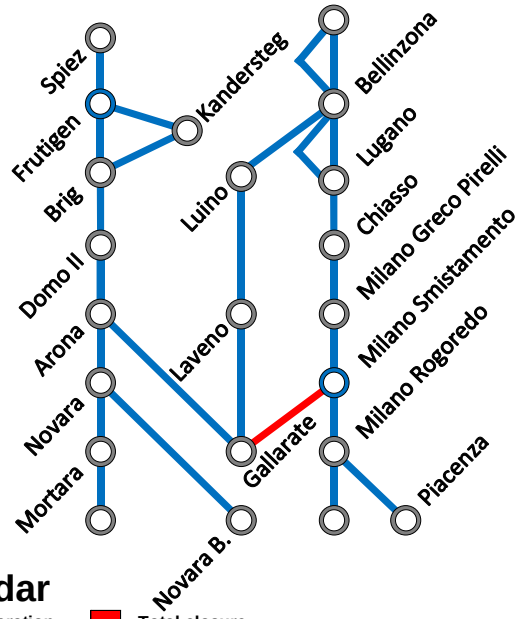

Major Capacity Restriction

- Location: Milano Certosa - Rho
- Type: 90 days of track closure of Varese line
- Period: 14.06.2026 - 13.09.2026
- Type of works: New station - Mind

2026 Calendar

 Single track operation Total closure

January						
Mo	Tu	We	Th	Fr	Sa	Su
			1	2	3	4
5	6	7	8	9	10	11
12	13	14	15	16	17	18
19	20	21	22	23	24	25
26	27	28	29	30	31	

February						
Mo	Tu	We	Th	Fr	Sa	Su
						1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	

March						
Mo	Tu	We	Th	Fr	Sa	Su
						1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	29
30	31					

April						
Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	5
6	7	8	9	10	11	12
13	14	15	16	17	18	19
20	21	22	23	24	25	26
27	28	29	30			

May						
Mo	Tu	We	Th	Fr	Sa	Su
				1	2	3
4	5	6	7	8	9	10
11	12	13	14	15	16	17
18	19	20	21	22	23	24
25	26	27	28	29	30	31

June						
Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7
8	9	10	11	12	13	14
15	16	17	18	19	20	21
22	23	24	25	26	27	28
29	30					

July						
Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	5
6	7	8	9	10	11	12
13	14	15	16	17	18	19
20	21	22	23	24	25	26
27	28	29	30	31		

August						
Mo	Tu	We	Th	Fr	Sa	Su
					1	2
3	4	5	6	7	8	9
10	11	12	13	14	15	16
17	18	19	20	21	22	23
24	25	26	27	28	29	30
31						

September						
Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	5
6	7	8	9	10	11	12
13	14	15	16	17	18	19
20	21	22	23	24	25	26
27	28	29	30			

October						
Mo	Tu	We	Th	Fr	Sa	Su
			1	2	3	4
5	6	7	8	9	10	11
12	13	14	15	16	17	18
19	20	21	22	23	24	25
26	27	28	29	30	31	

November						
Mo	Tu	We	Th	Fr	Sa	Su
						1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	29
30						


December						
Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	5
6	7	8	9	10	11	12
13	14	15	16	17	18	19
20	21	22	23	24	25	26
27	28	29	30	31		

Impact on International Rail Freight

- Cancellations: No
- Deviations: No deviations at the crossing points. There will be deviations on internal lines in R.F.I. network (via Alessandria - Piacenza)
- Estimated extra running time: related to the O/D of the trains
- In annual timetable: No

Impact of TCR 2026 at RFI (6)

Section Iselle - Domodossola - Arona

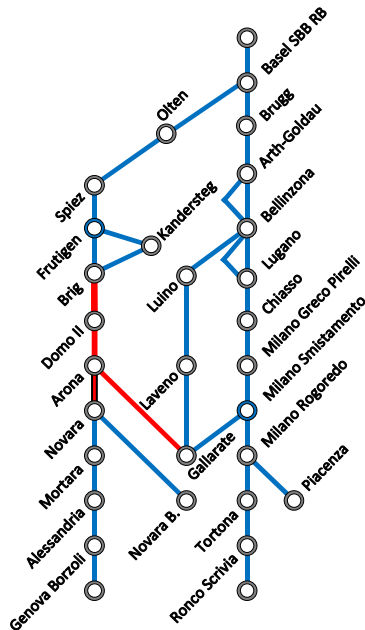

2026 Calendar

 Single track operation Total closure

January							February							March							April						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
			1	2	3	4							1							1			1	2	3	4	5
5	6	7	8	9	10	11	2	3	4	5	6	7	8	2	3	4	5	6	7	8	6	7	8	9	10	11	12
12	13	14	15	16	17	18	9	10	11	12	13	14	15	9	10	11	12	13	14	15	13	14	15	16	17	18	19
19	20	21	22	23	24	25	16	17	18	19	20	21	22	16	17	18	19	20	21	22	20	21	22	23	24	25	26
26	27	28	29	30	31		23	24	25	26	27	28		23	24	25	26	27	28	29	27	28	29	30			
														30	31												

May							June							July							August						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
				1	2	3	1	2	3	4	5	6	7	1	2	3	4	5	6	7	3	4	5	6	7	8	9
4	5	6	7	8	9	10	8	9	10	11	12	13	14	6	7	8	9	10	11	12	10	11	12	13	14	15	16
11	12	13	14	15	16	17	15	16	17	18	19	20	21	13	14	15	16	17	18	19	17	18	19	20	21	22	23
18	19	20	21	22	23	24	22	23	24	25	26	27	28	20	21	22	23	24	25	26	24	25	26	27	28	29	30
25	26	27	28	29	30	31	29	30						27	28	29	30	31			31						

September							October							November							December						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
	1	2	3	4	5	6				1	2	3	4							1			1	2	3	4	5
7	8	9	10	11	12	13	5	6	7	8	9	10	11	2	3	4	5	6	7	8	7	8	9	10	11	12	13
14	15	16	17	18	19	20	12	13	14	15	16	17	18	9	10	11	12	13	14	15	14	15	16	17	18	19	20
21	22	23	24	25	26	27	19	20	21	22	23	24	25	16	17	18	19	20	21	22	21	22	23	24	25	26	27
28	29	30					26	27	28	29	30	31		23	24	25	26	7	28	29	28	29	30	31			
														30													

Major Capacity Restriction

- Location:
Phase 1) Domodossola - Iselle
Phase 2) Arona - Domodossola
- Type:
Phase 1) 60 days of total closure
Phase 2) 44 days of total closure
- Period:
Phase 1) 29.05.2026 - 27.07.2026
Phase 2) 14.06.2026 - 27.07.2026 (in shadow)
- Type of works: Gauge enhancement - P/C 80 +

ERTMS


- Location: Arona - Oleggio
 - Type: 30 days of total closure
 - Period: 29.05.2026 - 26.06.2026 (in shadow)
 - Type of works: ERTMS
- Location: Sesto Calende - Arona + Arona - Oleggio
 - Type: 7 days of total closure
 - Period: 20.07.2026 - 27.07.2026
 - Type of works: Extraordinary maintenance to bridge

Impact on International Rail Freight

- Cancellations: Yes
- Deviations: Yes. Re-routing via Premosello - Borgomanero, or via Luino / Chiasso.
- Estimated extra running time: related to the O/D
- In annual timetable: Yes

Impact of TCR 2026 at RFI (7)

Section Domodossola - Novara: station of Novara Boschetto

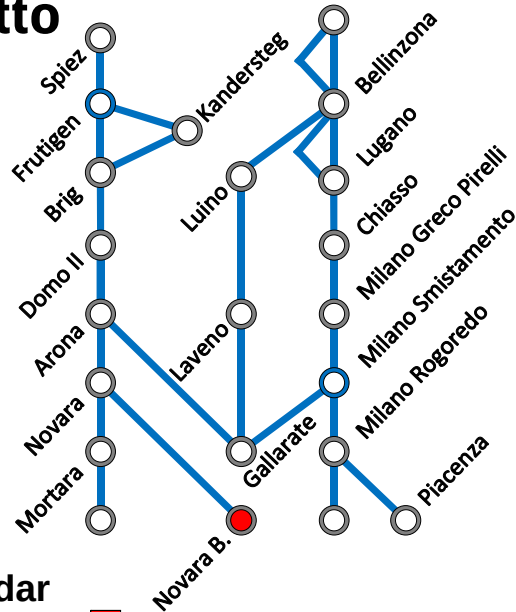

Major Capacity Restriction

- Location: Novara Boschetto
- Type: 23 days of total closure
- Period: 04.07.2026 - 27.07.2026 (in the same period of the total closure of the line Iselle - Domodossola)
- Type of works: Station upgrade

2026 Calendar

Single track operation Total closure

January						
Mo	Tu	We	Th	Fr	Sa	Su
			1	2	3	4
5	6	7	8	9	10	11
12	13	14	15	16	17	18
19	20	21	22	23	24	25
26	27	28	29	30	31	

February						
Mo	Tu	We	Th	Fr	Sa	Su
						1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	

March						
Mo	Tu	We	Th	Fr	Sa	Su
						1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	29
30	31					

April						
Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	5
6	7	8	9	10	11	12
13	14	15	16	17	18	19
20	21	22	23	24	25	26
27	28	29	30			

May						
Mo	Tu	We	Th	Fr	Sa	Su
				1	2	3
4	5	6	7	8	9	10
11	12	13	14	15	16	17
18	19	20	21	22	23	24
25	26	27	28	29	30	31

June						
Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7
8	9	10	11	12	13	14
15	16	17	18	19	20	21
22	23	24	25	26	27	28
29	30					

July						
Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	5
6	7	8	9	10	11	12
13	14	15	16	17	18	19
20	21	22	23	24	25	26
27	28	29	30	31		

August						
Mo	Tu	We	Th	Fr	Sa	Su
					1	2
3	4	5	6	7	8	9
10	11	12	13	14	15	16
17	18	19	20	21	22	23
24	25	26	27	28	29	30
31						

September						
Mo	Tu	We	Th	Fr	Sa	Su
	1	2	3	4	5	6
7	8	9	10	11	12	13
14	15	16	17	18	19	20
21	22	23	24	25	26	27
28	29	30				

October						
Mo	Tu	We	Th	Fr	Sa	Su
			1	2	3	4
5	6	7	8	9	10	11
12	13	14	15	16	17	18
19	20	21	22	23	24	25
26	27	28	29	30	31	

November						
Mo	Tu	We	Th	Fr	Sa	Su
						1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	29
30						


December						
Mo	Tu	We	Th	Fr	Sa	Su
	1	2	3	4	5	6
7	8	9	10	11	12	13
14	15	16	17	18	19	20
21	22	23	24	25	26	27
28	29	30	31			

Impact on International Rail Freight

- Cancellations: Yes, all the trains with O/D the station of Novara Boschetto.
- Deviations: No.
- Estimated extra running time: -
- In annual timetable: No

Impact of TCR 2026 at RFI (8)

Section Milano - Domodossola

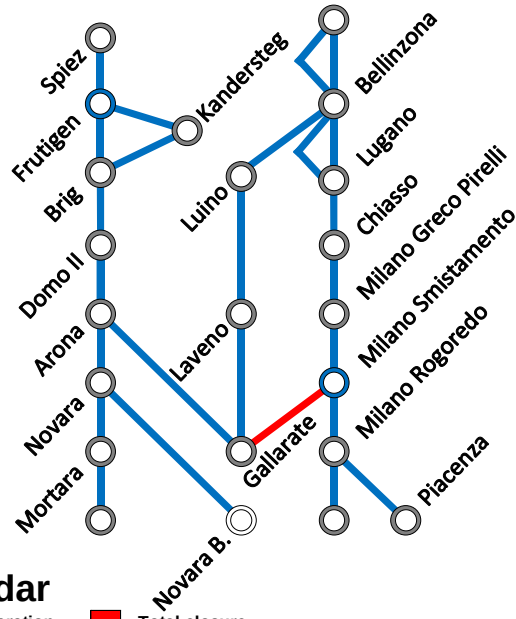

2026 Calendar

Single track operation Total closure

January							February							March							April						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
				1	2	3	4						1							1			1	2	3	4	5
5	6	7	8	9	10	11	2	3	4	5	6	7	8	2	3	4	5	6	7	8	6	7	8	9	10	11	12
12	13	14	15	16	17	18	9	10	11	12	13	14	15	9	10	11	12	13	14	15	13	14	15	16	17	18	19
19	20	21	22	23	24	25	16	17	18	19	20	21	22	16	17	18	19	20	21	22	20	21	22	23	24	25	26
26	27	28	29	30	31		23	24	25	26	27	28		23	24	25	26	27	28	29	27	28	29	30			
														30	31												

May							June							July							August						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
				1	2	3	1	2	3	4	5	6	7	1	2	3	4	5			1	2					
4	5	6	7	8	9	10	8	9	10	11	12	13	14	6	7	8	9	10	11	12	3	4	5	6	7	8	9
11	12	13	14	15	16	17	15	16	17	18	19	20	21	13	14	15	16	17	18	19	10	11	12	13	14	15	16
18	19	20	21	22	23	24	22	23	24	25	26	27	28	20	21	22	23	24	25	26	17	18	19	20	21	22	23
25	26	27	28	29	30	31	29	30						27	28	29	30	31			24	25	26	27	28	29	30
																					31						

September							October							November							December						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
	1	2	3	4	5	6					1	2	3							1			1	2	3	4	5
7	8	9	10	11	12	13	5	6	7	8	9	10	11	2	3	4	5	6	7	8	7	8	9	10	11	12	13
14	15	16	17	18	19	20	12	13	14	15	16	17	18	9	10	11	12	13	14	15	14	15	16	17	18	19	20
21	22	23	24	25	26	27	19	20	21	22	23	24	25	16	17	18	19	20	21	22	21	22	23	24	25	26	27
28	29	30					26	27	28	29	30	31		23	24	25	26	7	28	29	28	29	30	31			
														30													

Major Capacity Restriction


- Location: Gallarate - Rho
- Type: 25 days of total closure divided in two period
- Period:
 - Phase 1) 26.12.2025 - 06.01.2026
 - Phase 2) 29.05.2026 - 13.06.2026 (in shadow to total closure between Iselle and Domodossola)
- Type of works: line enhancement + ERTMS + upgrade Legnano station

Impact on International Rail Freight

- Cancellations: No.
- Deviations: In phase 1 rerouting via Borgomanero, Luino and Chiasso. In phase 2 rerouting via Chiasso and Luino.
- Estimated extra running time: related to the O/D of the trains
- In annual timetable: No

Impact of TCR 2026 at RFI (9)

Section Chiasso - Milano

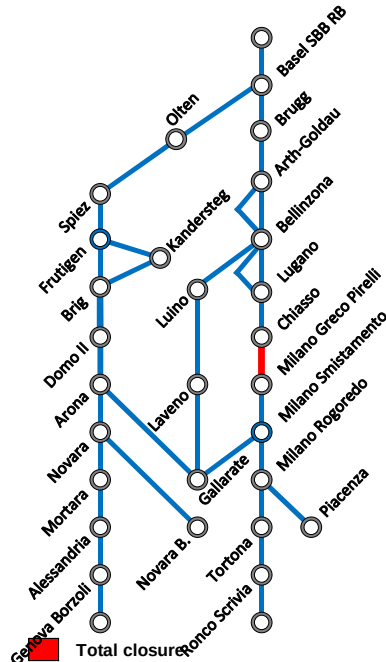

2026 Calendar

Single track operation

Total closure

January						
Mo	Tu	We	Th	Fr	Sa	Su
			1	2	3	4
5	6	7	8	9	10	11
12	13	14	15	16	17	18
19	20	21	22	23	24	25
26	27	28	29	30	31	

February						
Mo	Tu	We	Th	Fr	Sa	Su
						1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	

March						
Mo	Tu	We	Th	Fr	Sa	Su
						1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	29

April						
Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	5
6	7	8	9	10	11	12
13	14	15	16	17	18	19
20	21	22	23	24	25	26
27	28	29	30			

May						
Mo	Tu	We	Th	Fr	Sa	Su
				1	2	3
4	5	6	7	8	9	10
11	12	13	14	15	16	17
18	19	20	21	22	23	24
25	26	27	28	29	30	31

June						
Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7
8	9	10	11	12	13	14
15	16	17	18	19	20	21
22	23	24	25	26	27	28
29	30					

July						
Mo	Tu	We	Th	Fr	Sa	Su
	1	2	3	4	5	
6	7	8	9	10	11	12
13	14	15	16	17	18	19
20	21	22	23	24	25	26
27	28	29	30	31		

August						
Mo	Tu	We	Th	Fr	Sa	Su
					1	2
3	4	5	6	7	8	9
10	11	12	13	14	15	16
17	18	19	20	21	22	23
24	25	26	27	28	29	30

September						
Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	
7	8	9	10	11	12	13
14	15	16	17	18	19	20
21	22	23	24	25	26	27
28	29	30				

October						
Mo	Tu	We	Th	Fr	Sa	Su
	1	2	3	4		
5	6	7	8	9	10	11
12	13	14	15	16	17	18
19	20	21	22	23	24	25
26	27	28	29	30	31	

November						
Mo	Tu	We	Th	Fr	Sa	Su
						1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	29

December						
Mo	Tu	We	Th	Fr	Sa	Su
	1	2	3	4	5	6
7	8	9	10	11	12	13
14	15	16	17	18	19	20
21	22	23	24	25	26	27
28	29	30	31			

Major Capacity Restriction

- Location: Carimate - Bivio Rosales (via MO1)
- Type: 30 days of track closure with periodical night total closure for 6 hours from Monday/Tuesday to Friday/Saturday
- Period: 28.07.2026 - 26.08.2026
- Type of works: Upgrade Bivio P.C. Rosales

- Location:
 - Carimate - Como S. Giovanni (via MO1)
 - Carimate - Chiasso (via MO2)
- Type: 10 days of total closure (MO1 + MO2)
- Period: 27.08.2026 - 06.09.2026
- Type of works: Upgrade Bivio P.C. Rosales


Impact on International Rail Freight

- Cancellations: Yes.
- Deviations: Yes, reroutings via Chiasso and Luino.
- Estimated extra running time: related to the O/D of the trains
- In annual timetable: No

Impact of TCR 2026 at RFI (10)

Section Luino - Gallarate

State of play : 22.08.2024
Disclaimer see front page

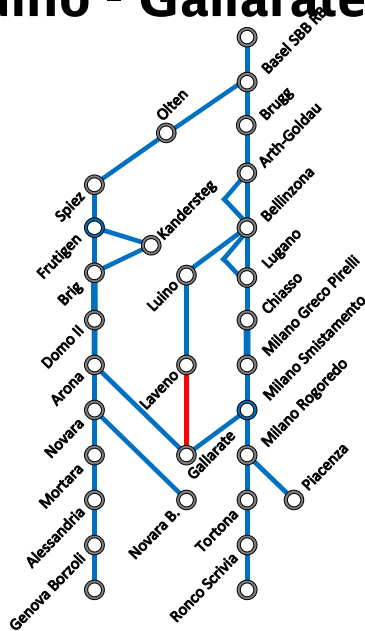

Major Capacity Restriction

- Location: Gallarate - Laveno
- Type: 21 days of total closure of the line via Ternate (the line via PM Ispra will be open)
- Period: 10.01.2026 - 30.01.2026
- Type of works: Extraordinary maintenance of bridge at km 23+877 + upgrade at the station of Sangiano and Travedona Biandronno + ERTMS

2026 Calendar

Single track operation Total closure

January							February							March							April						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
					1	2							1											1	2	3	4
5	6	7	8	9	10	11	2	3	4	5	6	7	8	2	3	4	5	6	7	8	6	7	8	9	10	11	12
12	13	14	15	16	17	18	9	10	11	12	13	14	15	9	10	11	12	13	14	15	13	14	15	16	17	18	19
19	20	21	22	23	24	25	16	17	18	19	20	21	22	16	17	18	19	20	21	22	20	21	22	23	24	25	26
26	27	28	29	30	31		23	24	25	26	27	28		23	24	25	26	27	28	29	27	28	29	30			
														30	31												

May							June							July							August						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
				1	2	3	1	2	3	4	5	6	7	6	7	8	9	10	11	12	3	4	5	6	7	8	9
4	5	6	7	8	9	10	8	9	10	11	12	13	14	13	14	15	16	17	18	19	10	11	12	13	14	15	16
11	12	13	14	15	16	17	15	16	17	18	19	20	21	20	21	22	23	24	25	26	17	18	19	20	21	22	23
18	19	20	21	22	23	24	22	23	24	25	26	27	28	27	28	29	30	31			24	25	26	27	28	29	30
25	26	27	28	29	30	31	29	30						27	28	29	30	31			31						

September							October							November							December						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
	1	2	3	4	5	6					1	2	3	2	3	4	5	6	7	8	1	2	3	4	5	6	
7	8	9	10	11	12	13	5	6	7	8	9	10	11	2	3	4	5	6	7	8	7	8	9	10	11	12	13
14	15	16	17	18	19	20	12	13	14	15	16	17	18	9	10	11	12	13	14	15	14	15	16	17	18	19	20
21	22	23	24	25	26	27	19	20	21	22	23	24	25	16	17	18	19	20	21	22	21	22	23	24	25	26	27
28	29	30					26	27	28	29	30	31		23	24	25	26	7	28	29	28	29	30	31			

Impact on International Rail Freight

- Cancellations: No
- Deviations: Yes, trains circulating via Gallarate - Ternate - Laveno will be rerouted via Gallarate - PM Ispra - Laveno
- Estimated extra running time: related to the O/D of the trains
- In annual timetable: No

Links to national TCR information

NL: www.prorail.nl/projecten

BE: to log in an account is needed

www.infrabel.be/en/professionals/rail-operators/business-corner

DE: http://fahrweg.dbnetze.com/fahrweg-en/customers/construction_site_information/

CH: <https://company.sbb.ch/de/sbb-als-geschaeftpartner/leistungen-evu/onestopshop/kapazitaetseinschraenkungen.html>

CH: <https://www.trasse.ch/de/10039/10040/?oid=10103&lang=de>

IT: to log in an account is needed: <https://epir.rfi.it/>
